

# I-94 FROM MICHIGAN AVENUE TO EAST OF M-60



Job Number: 210047

Managing Office: Jackson TSC

TSC Manager: Kelby Wallace

Construction Engineer: Jason Fossitt

Control Sections: 38101

Prime Contractor: Michigan Paving & Materials

Report Date: 02/09/2023

*Gibbs Road over I-94*



*Michigan Avenue over I-94*



*Michigan Avenue Traffic Circle*



*Concord Road at I-94*




*Gibbs Road over I-94*



*M-99 over I-94*



## PROJECT COSTS

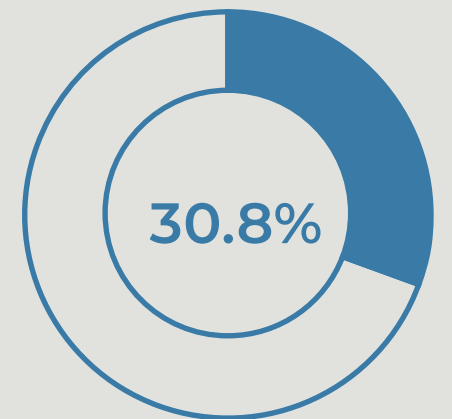

Percent Complete  
(Current Cost)

**\$162,001,795.40**

Awarded Contract Amount

**\$163,023,252.21**

Current Contract Cost (Auth + Pend)

**\$50,374,075.09**

Paid to Date
