



I-96 INTERCHANGE AT LATSON ROAD

AGENDA

- × Overview of the Project
- × General Questions
- × Open House




OVERVIEW OF THE PROJECT



- × Limits and scope of the project
- × Project Summary
- × Maintaining traffic plan
- × General construction schedule


LIMITS & SCOPE OF THE PROJECT

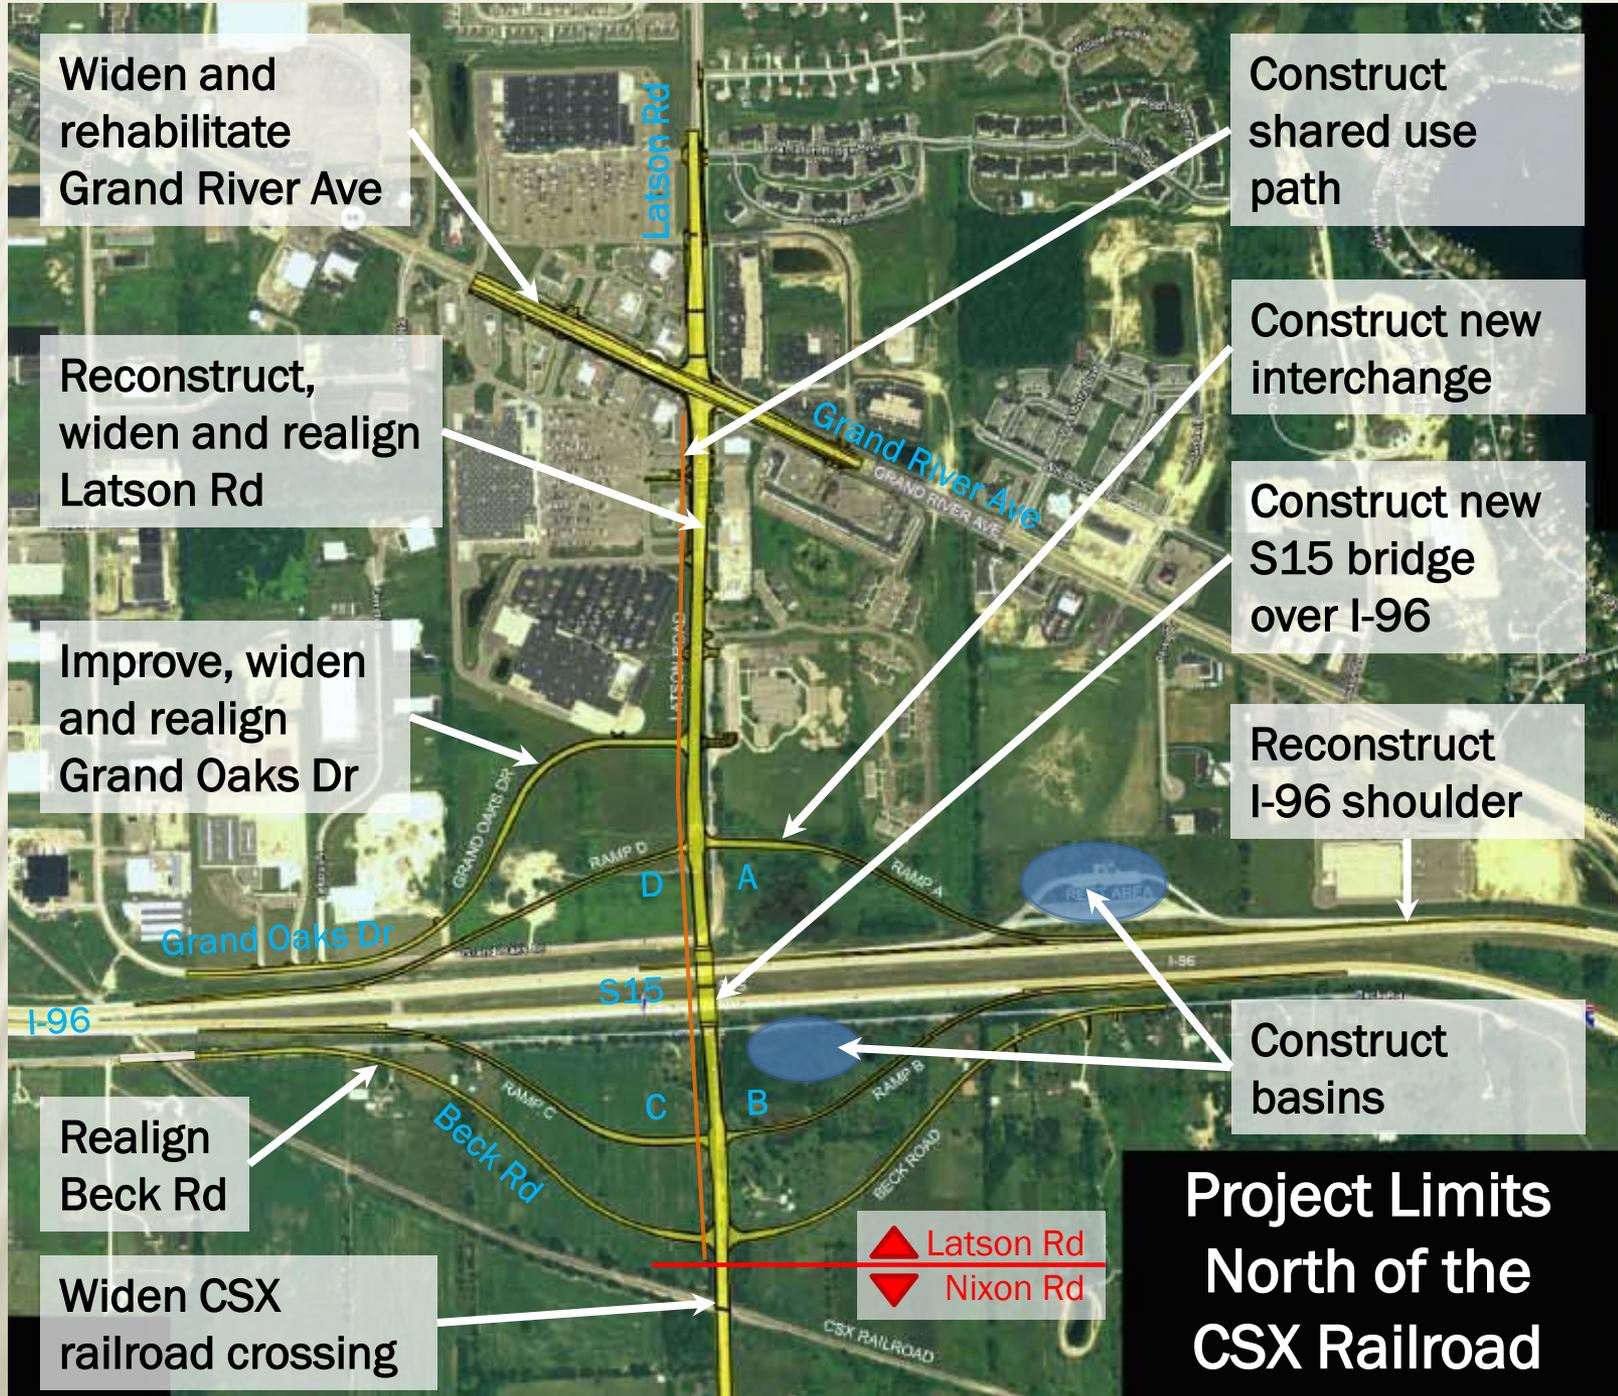

**Project Limits
North of the
CSX Railroad**

LIMITS & SCOPE OF THE PROJECT

North 

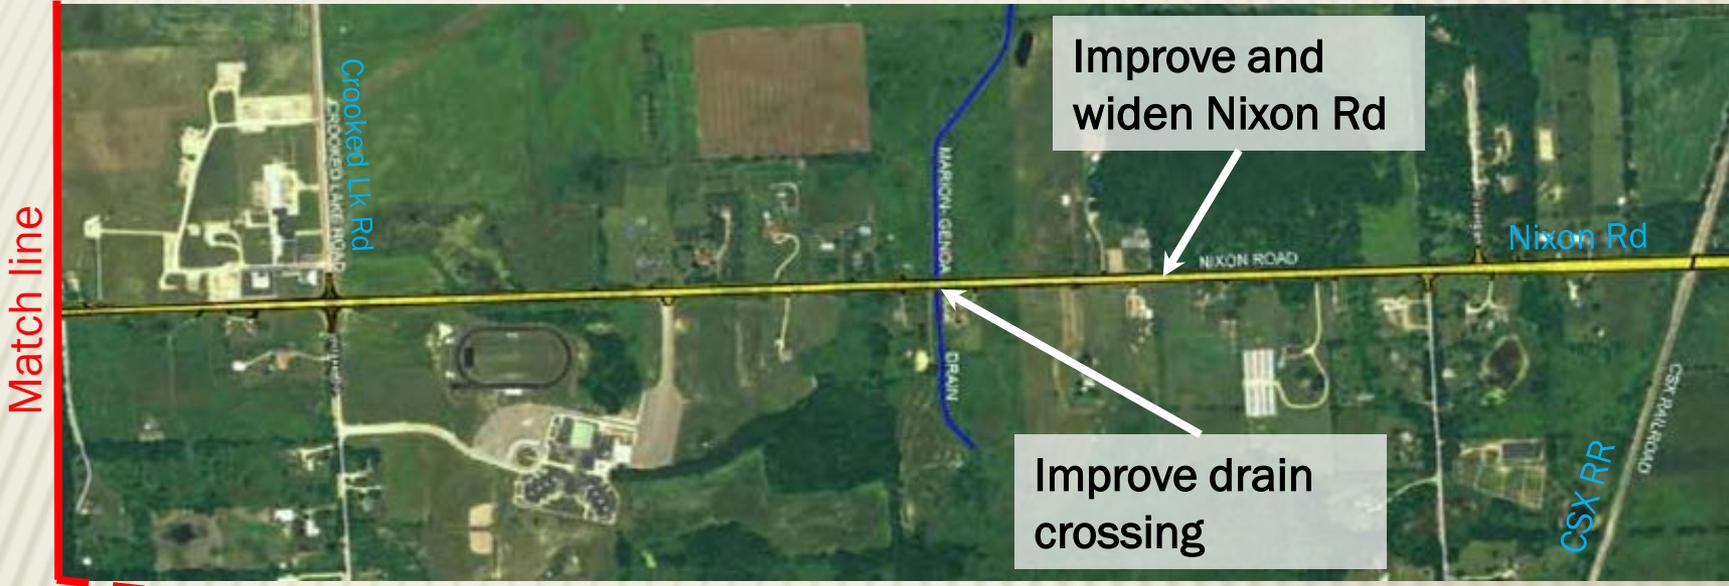

Match line



Project Limits
South of the
CSX Railroad

PROJECT SUMMARY



- × Project Let Date: 9/7/2012
- × Prime Contractor: Kamminga & Roodvoets (K&R)
- × Low Bid: \$25 million
- × Funding source: Federal, State, Local (cash contributions & ROW), Private (cash contributions & ROW donations)
- × Tentative Construction Schedule: 10/2012-11/2013

MAINTAINING TRAFFIC PLAN

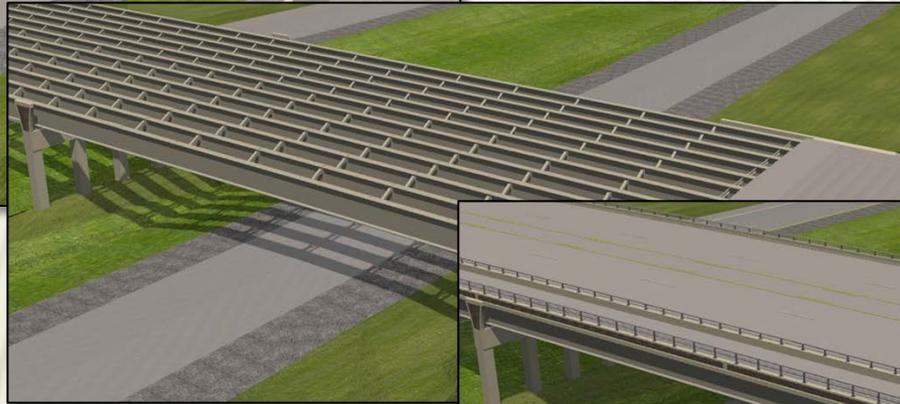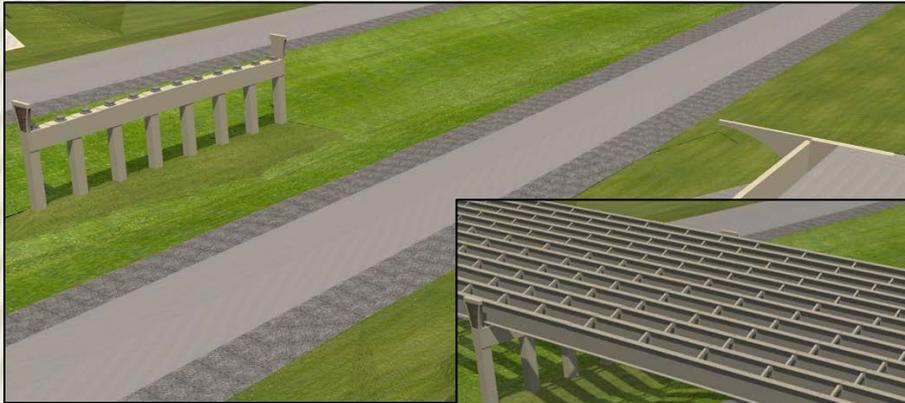

× I-96

- + During ramp, shoulder, and substructure work, 3 lanes of I-96 traffic must be shifted toward median and maintained at all times.
- + To place new bridge beams, all ramps must be paved and I-96 traffic may be routed onto ramps.

MAINTAINING TRAFFIC PLAN

- × Grand River Ave & Latson Rd intersection
 - + Staged construction by quadrant to widen the intersection
 - + Latson Rd traffic shifted-one lane in each direction maintained
 - + Grand River Ave traffic shifted- two lanes in each direction maintained
 - + For milling & resurfacing of Grand River- one lane in each direction. (only allowed weeknights 8pm-5am)

MAINTAINING TRAFFIC PLAN

- × Latson Rd widening & reconstruction
 - + Staged construction to build one side of the road at a time
 - + Latson Rd traffic shifted-one lane in each direction maintained
 - + Latson Rd closed south of Latson Elementary School



MAINTAINING TRAFFIC PLAN

- × Nixon Rd
 - + Close Nixon Rd to through traffic
 - + Maintain local access at all times.

- × Grand Oaks Dr
 - + Close and detour.

- × Beck Rd
 - + Access to Beck Rd east of Nixon Rd must be maintained at all times.
 - + Staging developed to realign Beck Rd before work on Nixon Rd between CSX railroad and I-96 may be performed.

GENERAL CONSTRUCTION SCHEDULE

- × Preparatory work (Stage A)
 - + Fall 2012 to Spring 2013
 - + Clearing & tree removal (per MDEQ Permit requirements)
 - + Miscellaneous earthwork activities
 - + Utility relocations
 - + Beck Rd
 - + Rest Area demolition
 - + Construct bridge median pier

GENERAL CONSTRUCTION SCHEDULE

× 2013 Work

- + April-August- Ramps, bridge abutments, new Nixon/Latson, Grand Oaks
- + August-October- Complete bridge
- + July-September- Latson, Nixon
- + Late August-November- Grand River/Latson intersection & Grand River resurfacing

**Discussion /
Questions?**
