



10576-190706 I-75 Reconstruction - Wayne County


Road Reconstruction Baseline Schedule Example

Data Date: 1/12/16

Run Date: 1/25/16

Submission Date: 1/27/16

Contractor: ABC Construction, Inc.

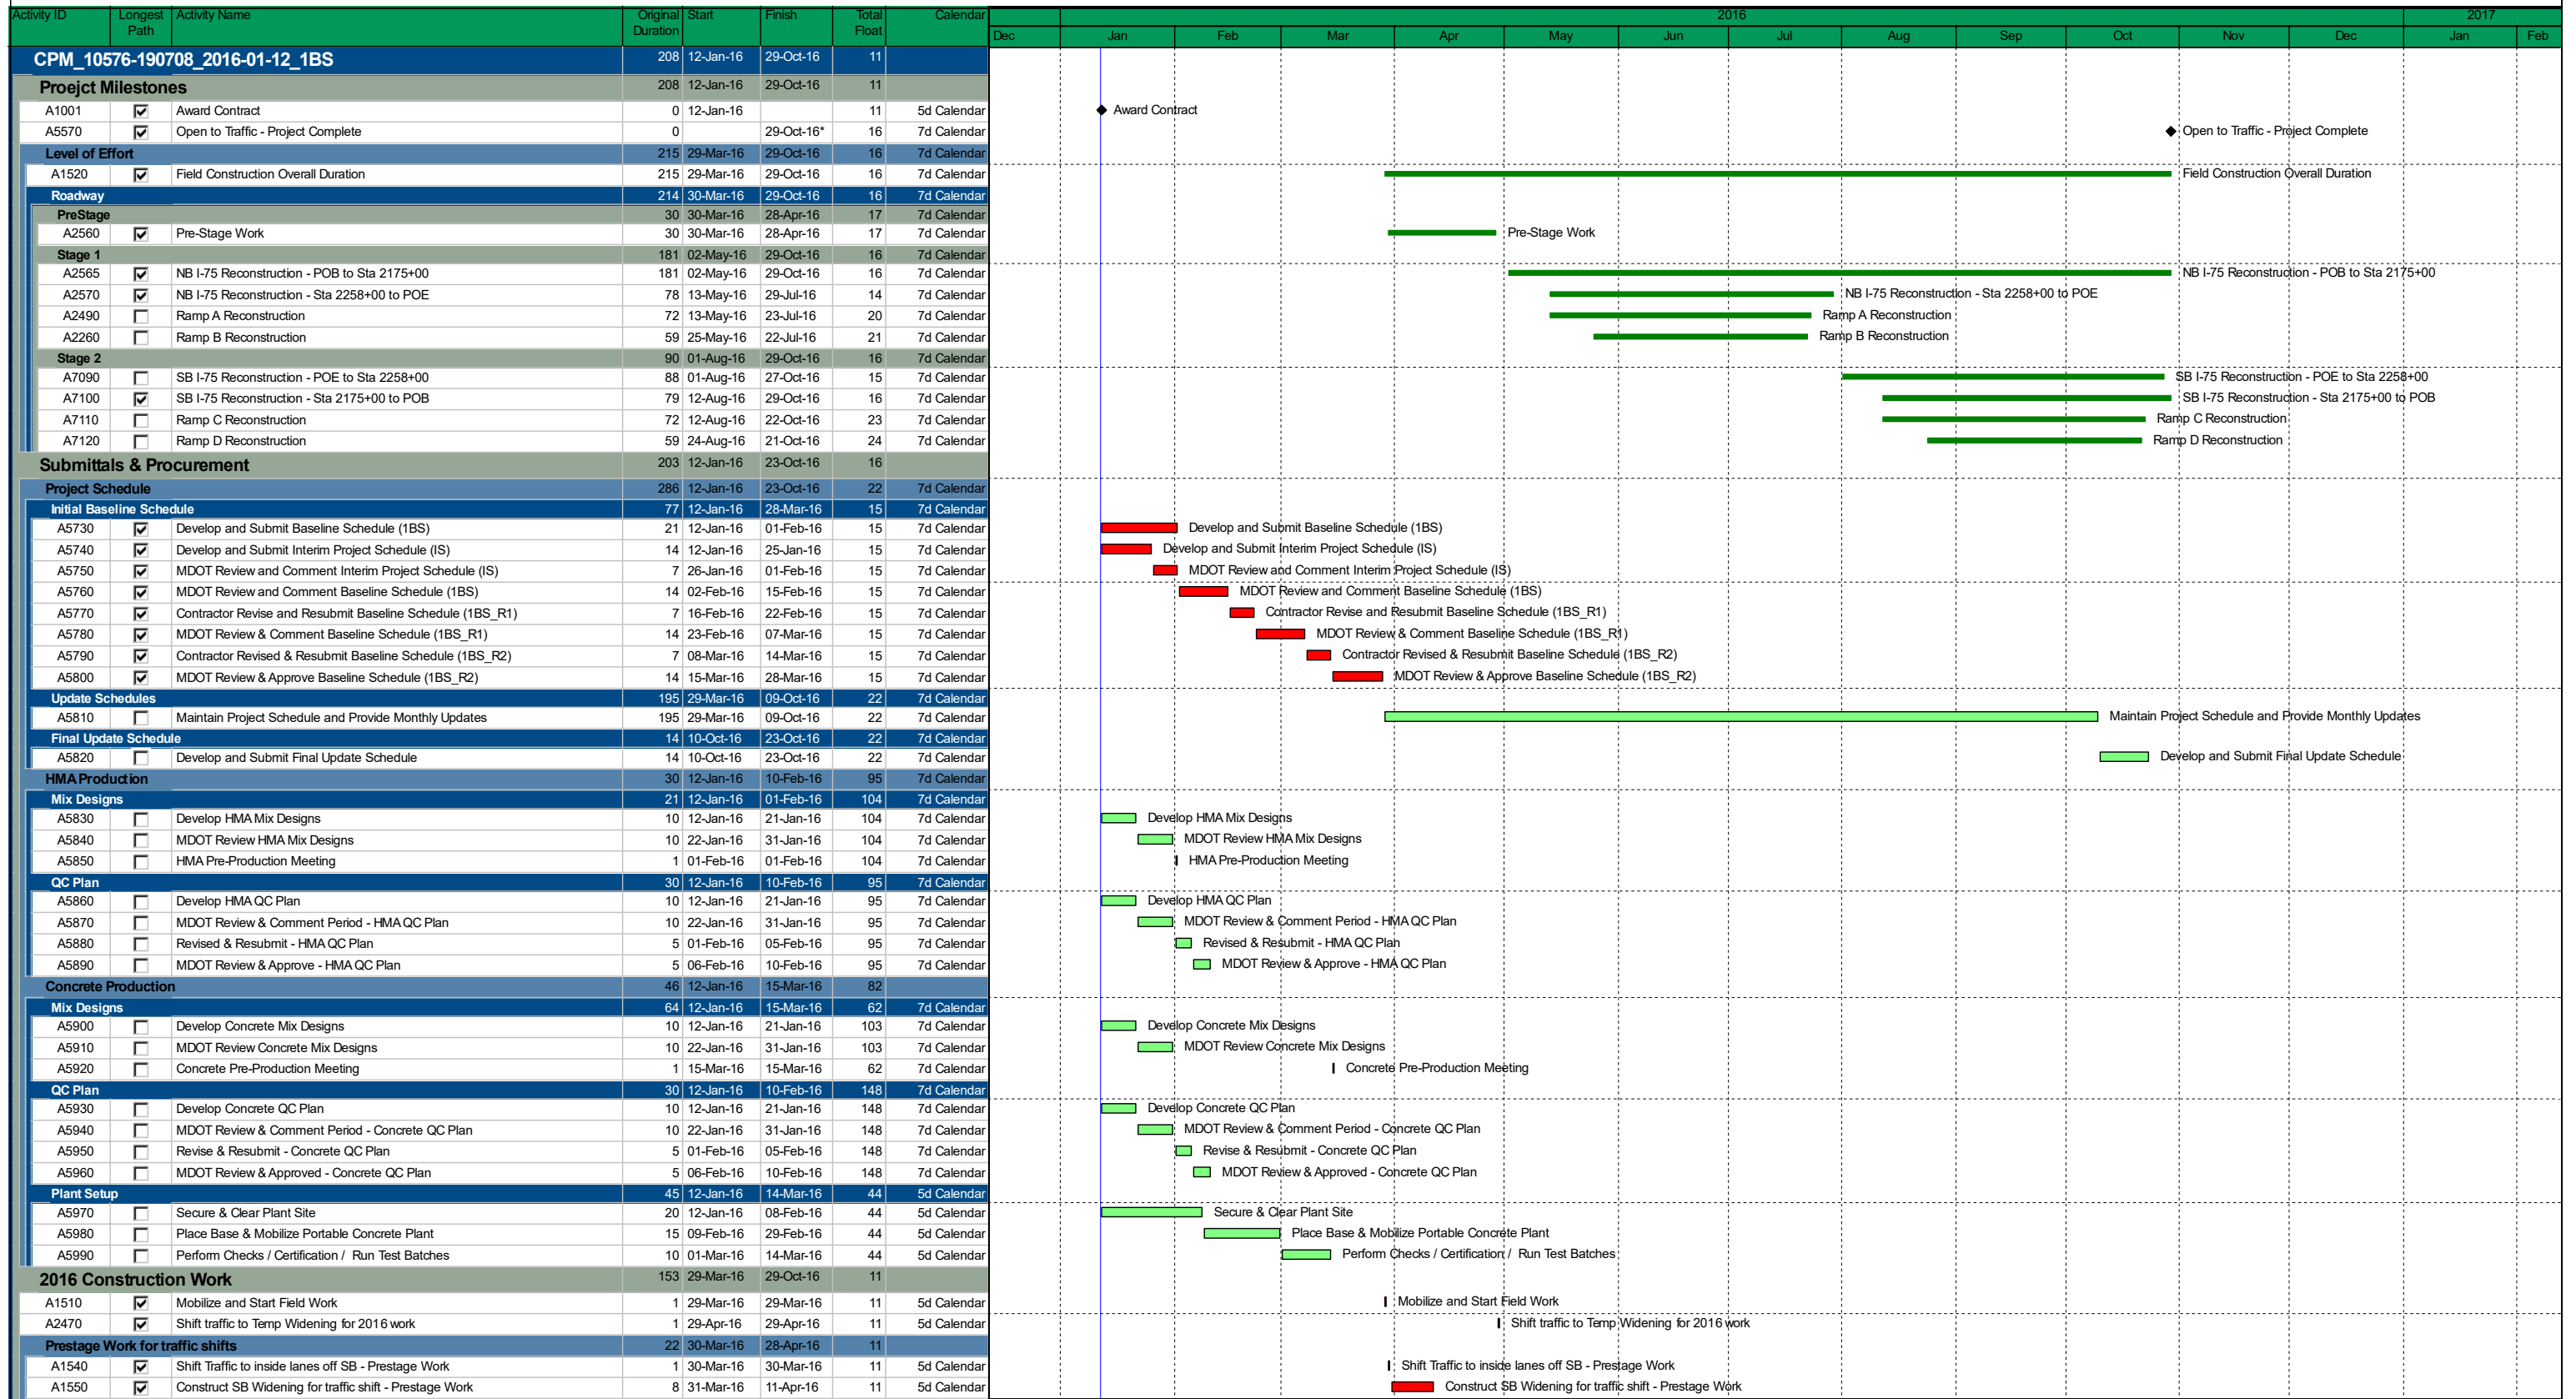

Remaining Level of Effort

Actual Work

Critical Remaining Work

WBS Summary Activity

Actual Level of Effort

Remaining Work

◆

Milestone

WBS Summary Progress



10576-190706 I-75 Reconstruction - Wayne County

Road Reconstruction Baseline Schedule Example

Data Date: 1/12/16

Run Date: 1/25/16

Submission Date: 1/27/16

Contractor: ABC Construction, Inc.

Activity ID	Longest Path	Activity Name	Original Duration	Start	Finish	Total Float	Calendar	2016												2017			
								Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	
A1930	<input checked="" type="checkbox"/>	Install TCB/Signs & Shift Traffic - Prestage Work	3	11-Apr-16	13-Apr-16	11	5d Calendar							<div><div></div> Install TCB/Signs & Shift Traffic - Prestage Work</div>									
A2040	<input checked="" type="checkbox"/>	Shift traffic on NB to outside lanes - Prestage Work	1	14-Apr-16	14-Apr-16	11	5d Calendar							<div><div></div> Shift traffic on NB to outside lanes - Prestage Work</div>									
A2050	<input type="checkbox"/>	Construct Inside widening on NB - Prestage Work	7	14-Apr-16	22-Apr-16	15	5d Calendar							<div><div></div> Construct Inside widening on NB - Prestage Work</div>									
A2080	<input checked="" type="checkbox"/>	Construct crossovers in median - Prestage Work	7	15-Apr-16	25-Apr-16	11	5d Calendar							<div><div></div> Construct crossovers in median - Prestage Work</div>									
A2100	<input type="checkbox"/>	Install pipe at Michigan Drain - Prestage Work	2	16-Apr-16	17-Apr-16	4	Weekend only							<div><div></div> Install pipe at Michigan Drain - Prestage Work</div>									
A2270	<input checked="" type="checkbox"/>	Install TCB in crossovers - Prestage Work	3	21-Apr-16	25-Apr-16	11	5d Calendar							<div><div></div> Install TCB in crossovers - Prestage Work</div>									
A2410	<input checked="" type="checkbox"/>	Striping / Signs - Prestage Work	3	26-Apr-16	28-Apr-16	11	5d Calendar							<div><div></div> Striping / Signs - Prestage Work</div>									
2016 Roadwork - Stage 1			65	02-May-16	29-Jul-16	10																	
NB Reconstruct (POB to Sta 2175+00)			64	02-May-16	28-Jul-16	11																	
A2520	<input checked="" type="checkbox"/>	Build haul Road - Stage 1 NB	4	02-May-16	05-May-16	11	5d Calendar							<div><div></div> Build haul Road - Stage 1 NB</div>									
A2700	<input checked="" type="checkbox"/>	Break and Remove pavement - Stage 1 NB - POB to Sta 2175+00	5	06-May-16	12-May-16	11	5d Calendar							<div><div></div> Break and Remove pavement - Stage 1 NB - POB to Sta 2175+00</div>									
A2870	<input checked="" type="checkbox"/>	Strip topsoil and ditches - Stage 1 NB - POB to Sta 2175+00	3	13-May-16	17-May-16	11	5d Calendar							<div><div></div> Strip topsoil and ditches - Stage 1 NB - POB to Sta 2175+00</div>									
A3020	<input checked="" type="checkbox"/>	Build ditches - Stage 1 NB - POB to Sta 2175+00	3	18-May-16	20-May-16	11	5d Calendar							<div><div></div> Build ditches - Stage 1 NB - POB to Sta 2175+00</div>									
A3110	<input checked="" type="checkbox"/>	Mass Excavate/Embankment grade - Stage 1 NB - POB to Sta 2175+00	10	19-May-16	01-Jun-16	11	5d Calendar							<div><div></div> Mass Excavate/Embankment grade - Stage 1 NB - POB to Sta 2175+00</div>									
A3530	<input checked="" type="checkbox"/>	Complete storm sewer - Stage 1 NB - POB to Sta 2175+00	5	31-May-16	06-Jun-16	11	5d Calendar							<div><div></div> Complete storm sewer - Stage 1 NB - POB to Sta 2175+00</div>									
A3890	<input checked="" type="checkbox"/>	Fine grade clay - Stage 1 NB - POB to Sta 2175+00	4	07-Jun-16	10-Jun-16	11	5d Calendar							<div><div></div> Fine grade clay - Stage 1 NB - POB to Sta 2175+00</div>									
A4120	<input checked="" type="checkbox"/>	Place fabric and stone - Stage 1 NB - POB to Sta 2175+00	4	13-Jun-16	16-Jun-16	11	5d Calendar							<div><div></div> Place fabric and stone - Stage 1 NB - POB to Sta 2175+00</div>									
A4130	<input checked="" type="checkbox"/>	Place edgedrain - Stage 1 NB - POB to Sta 2175+00	4	13-Jun-16	16-Jun-16	11	5d Calendar							<div><div></div> Place edgedrain - Stage 1 NB - POB to Sta 2175+00</div>									
A4330	<input checked="" type="checkbox"/>	Trim stone - Stage 1 NB - POB to Sta 2175+00	4	17-Jun-16	22-Jun-16	11	5d Calendar							<div><div></div> Trim stone - Stage 1 NB - POB to Sta 2175+00</div>									
A4520	<input checked="" type="checkbox"/>	Pave 24' lane - Stage 1 NB - POB to Sta 2175+00	1	23-Jun-16	23-Jun-16	11	5d Calendar							<div><div></div> Pave 24' lane - Stage 1 NB - POB to Sta 2175+00</div>									
A4550	<input type="checkbox"/>	Cure 24' lane - Stage 1 NB - POB to Sta 2175+00	3	24-Jun-16	26-Jun-16	16	7d Calendar							<div><div></div> Cure 24' lane - Stage 1 NB - POB to Sta 2175+00</div>									
A4660	<input type="checkbox"/>	Pave outside shoulder - Stage 1 NB - POB to Sta 2175+00	1	27-Jun-16	27-Jun-16	14	5d Calendar							<div><div></div> Pave outside shoulder - Stage 1 NB - POB to Sta 2175+00</div>									
A4630	<input checked="" type="checkbox"/>	Trim 2nd 24' lane - Stage 1 NB - POB to Sta 2175+00	2	27-Jun-16	28-Jun-16	12	5d Calendar							<div><div></div> Trim 2nd 24' lane - Stage 1 NB - POB to Sta 2175+00</div>									
A4690	<input type="checkbox"/>	Cure on outside shoulder - Stage 1 NB - POB to Sta 2175+00	2	28-Jun-16	29-Jun-16	20	7d Calendar							<div><div></div> Cure on outside shoulder - Stage 1 NB - POB to Sta 2175+00</div>									
A4700	<input checked="" type="checkbox"/>	Pave 2nd 24' lane - Stage 1 NB - POB to Sta 2175+00	1	29-Jun-16	29-Jun-16	12	5d Calendar							<div><div></div> Pave 2nd 24' lane - Stage 1 NB - POB to Sta 2175+00</div>									
A4760	<input checked="" type="checkbox"/>	Cure 2nd 24' lane - Stage 1 NB - POB to Sta 2175+00	3	30-Jun-16	02-Jul-16	17	7d Calendar							<div><div></div> Cure 2nd 24' lane - Stage 1 NB - POB to Sta 2175+00</div>									
A4780	<input type="checkbox"/>	Fine grade outside slopes - Stage 1 NB - POB to Sta 2175+00	2	30-Jun-16	01-Jul-16	19	5d Calendar							<div><div></div> Fine grade outside slopes - Stage 1 NB - POB to Sta 2175+00</div>									
A4860	<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 1 NB - POB to Sta 2175+00	2	04-Jul-16	05-Jul-16	19	5d Calendar							<div><div></div> Topsoil outside slopes and ditches - Stage 1 NB - POB to Sta 2175+00</div>									
A4790	<input checked="" type="checkbox"/>	Cleanup inside shoulder - Stage 1 NB - POB to Sta 2175+00	1	04-Jul-16	04-Jul-16	12	5d Calendar							<div><div></div> Cleanup inside shoulder - Stage 1 NB - POB to Sta 2175+00</div>									
A4830	<input checked="" type="checkbox"/>	Pave inside shoulder - Stage 1 NB - POB to Sta 2175+00	1	05-Jul-16	05-Jul-16	12	5d Calendar							<div><div></div> Pave inside shoulder - Stage 1 NB - POB to Sta 2175+00</div>									
A4930	<input type="checkbox"/>	Restore outside slopes and ditches - Stage 1 NB - POB to Sta 2175+00	2	06-Jul-16	07-Jul-16	19	5d Calendar							<div><div></div> Restore outside slopes and ditches - Stage 1 NB - POB to Sta 2175+00</div>									
A4870	<input checked="" type="checkbox"/>	Cure on inside shoulder - Stage 1 NB - POB to Sta 2175+00	3	06-Jul-16	08-Jul-16	16	7d Calendar							<div><div></div> Cure on inside shoulder - Stage 1 NB - POB to Sta 2175+00</div>									
A5030	<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 1 NB - POB to Sta 2175+00	5	08-Jul-16	14-Jul-16	19	5d Calendar							<div><div></div> Place all signs (Temp and Perm) - Stage 1 NB - POB to Sta 2175+00</div>									
A4980	<input checked="" type="checkbox"/>	Place median drainage (VG or Ditches) - Stage 1 NB - POB to Sta 2175+00	3	11-Jul-16	13-Jul-16	10	5d Calendar							<div><div></div> Place median drainage (VG or Ditches) - Stage 1 NB - POB to Sta 2175+00</div>									
A5160	<input checked="" type="checkbox"/>	Place median barrier wall where applicable - Stage 1 NB - POB to Sta 2175+00	5	14-Jul-16	20-Jul-16	10	5d Calendar							<div><div></div> Place median barrier wall where applicable - Stage 1 NB - POB to Sta 2175+00</div>									
A5370	<input checked="" type="checkbox"/>	Run ride quality on all lanes - Stage 1 NB - POB to Sta 2175+00	2	21-Jul-16	22-Jul-16	10	5d Calendar							<div><div></div> Run ride quality on all lanes - Stage 1 NB - POB to Sta 2175+00</div>									
A5430	<input checked="" type="checkbox"/>	Grind as needed on lanes - Stage 1 NB - POB to Sta 2175+00	2	25-Jul-16	26-Jul-16	10	5d Calendar							<div><div></div> Grind as needed on lanes - Stage 1 NB - POB to Sta 2175+00</div>									
A5500	<input checked="" type="checkbox"/>	Cleanup / Striping - Stage 1 NB - POB to Sta 2175+00	2	27-Jul-16	28-Jul-16	11	5d Calendar							<div><div></div> Cleanup / Striping - Stage 1 NB - POB to Sta 2175+00</div>									
A5490	<input checked="" type="checkbox"/>	Saw and seal all lanes - Stage 1 NB - POB to Sta 2175+00	2	27-Jul-16	28-Jul-16	11	5d Calendar							<div><div></div> Saw and seal all lanes - Stage 1 NB - POB to Sta 2175+00</div>									
NB Reconstruct (Sta 2258+00 to POE)			56	13-May-16	29-Jul-16	10																	
A2750	<input checked="" type="checkbox"/>	Break and Remove pavement - Stage 1 NB - Sta 2258+00 to POE	8	13-May-16	24-May-16	15	5d Calendar							<div><div></div> Break and Remove pavement - Stage 1 NB - Sta 2258+00 to POE</div>									
A3080	<input type="checkbox"/>	Mass Excavate/Embankment grade - Stage 1 NB - Sta 2258+00 to POE	5	25-May-16	31-May-16	15	5d Calendar							<div><div></div> Mass Excavate/Embankment grade - Stage 1 NB - Sta 2258+00 to POE</div>									
A3090	<input type="checkbox"/>	Build ditches - Stage 1 NB - Sta 2258+00 to POE	5	25-May-16	31-May-16	15	5d Calendar							<div><div></div> Build ditches - Stage 1 NB - Sta 2258+00 to POE</div>									
A3100	<input type="checkbox"/>	Strip topsoil and ditches - Stage 1 NB - Sta 2258+00 to POE	5	25-May-16	31-May-16	15	5d Calendar							<div><div></div> Strip topsoil and ditches - Stage 1 NB - Sta 2258+00 to POE</div>									
A3320	<input type="checkbox"/>	Complete storm sewer - Stage 1 NB - Sta 2258+00 to POE	5	01-Jun-16	07-Jun-16	15	5d Calendar							<div><div></div> Complete storm sewer - Stage 1 NB - Sta 2258+00 to POE</div>									
A3550	<input type="checkbox"/>	Place edgedrain - Stage 1 NB - Sta 2258+00 to POE	5	08-Jun-16	14-Jun-16	15	5d Calendar							<div><div></div> Place edgedrain - Stage 1 NB - Sta 2258+00 to POE</div>									
A3560	<input type="checkbox"/>	Fine grade clay - Stage 1 NB - Sta 2258+00 to POE	5	08-Jun-16	14-Jun-16	15	5d Calendar							<div><div></div> Fine grade clay - Stage 1 NB - Sta 2258+00 to POE</div>									
A4500	<input type="checkbox"/>	Place fabric and stone - Stage 1 NB - Sta 2258+00 to POE	4	15-Jun-16	20-Jun-16	15	5d Calendar																

■ Remaining Level of Effort

■ Actual Level of Effort

■ Actual Work

■ Remaining Work

■ Critical Remaining Work

◆ Milestone

■ WBS Summary Activity

■ WBS Summary Progress



10576-190706 I-75 Reconstruction - Wayne County

Road Reconstruction Baseline Schedule Example

Data Date: 1/12/16

Run Date: 1/25/16

Submission Date: 1/27/16

Contractor: ABC Construction, Inc.

Activity ID	Longest Path	Activity Name	Original Duration	Start	Finish	Total Float	Calendar	2016												2017				
								Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb		
A5340	<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 1 NB - Sta 2258+00 to POE	5	08-Jul-16	14-Jul-16	20	5d Calendar											Place all signs (Temp and Perm) - Stage 1 NB - Sta 2258+00 to POE						
A5360	<input type="checkbox"/>	Place median drainage (VG or Ditches) - Stage 1 NB - Sta 2258+00 to POE	3	08-Jul-16	12-Jul-16	17	5d Calendar											Place median drainage (VG or Ditches) - Stage 1 NB - Sta 2258+00 to POE						
A5420	<input type="checkbox"/>	Place median barrier wall where applicable - Stage 1 NB - Sta 2258+00 to POE	5	13-Jul-16	19-Jul-16	17	5d Calendar											Place median barrier wall where applicable - Stage 1 NB - Sta 2258+00 to POE						
A5410	<input type="checkbox"/>	Run ride quality on all lanes - Stage 1 NB - Sta 2258+00 to POE	2	18-Jul-16	19-Jul-16	17	5d Calendar											Run ride quality on all lanes - Stage 1 NB - Sta 2258+00 to POE						
A5390	<input checked="" type="checkbox"/>	Saw and seal all lanes - Stage 1 NB - Sta 2258+00 to POE	2	27-Jul-16	28-Jul-16	10	5d Calendar											Saw and seal all lanes - Stage 1 NB - Sta 2258+00 to POE						
A5400	<input checked="" type="checkbox"/>	Grind as needed on lanes - Stage 1 NB - Sta 2258+00 to POE	2	27-Jul-16	28-Jul-16	10	5d Calendar											Grind as needed on lanes - Stage 1 NB - Sta 2258+00 to POE						
A5470	<input checked="" type="checkbox"/>	Place temp stripes - Stage 1 NB - Sta 2258+00 to POE	1	29-Jul-16	29-Jul-16	10	5d Calendar											Place temp stripes - Stage 1 NB - Sta 2258+00 to POE						
A5480	<input checked="" type="checkbox"/>	Final sweeping - Stage 1 NB - Sta 2258+00 to POE	1	29-Jul-16	29-Jul-16	10	5d Calendar											Final sweeping - Stage 1 NB - Sta 2258+00 to POE						
Ramps			51	13-May-16	23-Jul-16	15																		
Exit Ramp A			51	13-May-16	23-Jul-16	15																		
A2450	<input type="checkbox"/>	Break and Remove pavement - Stage 1 - Exit Ramp A	4	13-May-16	18-May-16	22	5d Calendar											Break and Remove pavement - Stage 1 - Exit Ramp A						
A2660	<input type="checkbox"/>	Strip topsoil and ditches - Stage 1 - Exit Ramp A	3	19-May-16	23-May-16	22	5d Calendar											Strip topsoil and ditches - Stage 1 - Exit Ramp A						
A2830	<input type="checkbox"/>	Build ditches - Stage 1 - Exit Ramp A	3	24-May-16	26-May-16	22	5d Calendar											Build ditches - Stage 1 - Exit Ramp A						
A2880	<input type="checkbox"/>	Mass Excavate/Embankment grade - Stage 1 - Exit Ramp A	3	27-May-16	31-May-16	22	5d Calendar											Mass Excavate/Embankment grade - Stage 1 - Exit Ramp A						
A3040	<input type="checkbox"/>	Complete storm sewer - Stage 1 - Exit Ramp A	3	01-Jun-16	03-Jun-16	22	5d Calendar											Complete storm sewer - Stage 1 - Exit Ramp A						
A3230	<input type="checkbox"/>	Fine grade clay - Stage 1 - Exit Ramp A	2	06-Jun-16	07-Jun-16	22	5d Calendar											Fine grade clay - Stage 1 - Exit Ramp A						
A3300	<input type="checkbox"/>	Place edgedrain - Stage 1 - Exit Ramp A	1	08-Jun-16	08-Jun-16	22	5d Calendar											Place edgedrain - Stage 1 - Exit Ramp A						
A3340	<input type="checkbox"/>	Place fabric and stone - Stage 1 - Exit Ramp A	3	09-Jun-16	13-Jun-16	22	5d Calendar											Place fabric and stone - Stage 1 - Exit Ramp A						
A3500	<input type="checkbox"/>	Trim stone - Stage 1 - Exit Ramp A	2	14-Jun-16	15-Jun-16	22	5d Calendar											Trim stone - Stage 1 - Exit Ramp A						
A3580	<input type="checkbox"/>	Pave Ramp Lanes - Stage 1 - Exit Ramp A	1	28-Jun-16	28-Jun-16	14	5d Calendar											Pave Ramp Lanes - Stage 1 - Exit Ramp A						
A3670	<input type="checkbox"/>	Cure Ramp Lanes - Stage 1 - Exit Ramp A	3	29-Jun-16	01-Jul-16	20	7d Calendar											Cure Ramp Lanes - Stage 1 - Exit Ramp A						
A3750	<input type="checkbox"/>	Trim Outside shoulder - Stage 1 - Exit Ramp A	1	04-Jul-16	04-Jul-16	14	5d Calendar											Trim Outside shoulder - Stage 1 - Exit Ramp A						
A3840	<input type="checkbox"/>	Pave outside shoulder - Stage 1 - Exit Ramp A	1	05-Jul-16	05-Jul-16	14	5d Calendar											Pave outside shoulder - Stage 1 - Exit Ramp A						
A3910	<input type="checkbox"/>	Cure Outside Shoulder - Stage 1 - Exit Ramp A	3	06-Jul-16	08-Jul-16	20	7d Calendar											Cure Outside Shoulder - Stage 1 - Exit Ramp A						
A4070	<input type="checkbox"/>	Saw and seal all lanes - Stage 1 - Exit Ramp A	2	11-Jul-16	12-Jul-16	21	5d Calendar											Saw and seal all lanes - Stage 1 - Exit Ramp A						
A4080	<input type="checkbox"/>	Fine grade outside slopes - Stage 1 - Exit Ramp A	3	11-Jul-16	13-Jul-16	14	5d Calendar											Fine grade outside slopes - Stage 1 - Exit Ramp A						
A4210	<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 1 - Exit Ramp A	3	14-Jul-16	18-Jul-16	14	5d Calendar											Topsoil outside slopes and ditches - Stage 1 - Exit Ramp A						
A4380	<input type="checkbox"/>	Restore outside slopes and ditches - Stage 1 - Exit Ramp A	2	19-Jul-16	20-Jul-16	14	5d Calendar											Restore outside slopes and ditches - Stage 1 - Exit Ramp A						
A4440	<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 1 - Exit Ramp A	1	21-Jul-16	21-Jul-16	14	5d Calendar											Place all signs (Temp and Perm) - Stage 1 - Exit Ramp A						
A4530	<input type="checkbox"/>	Final sweeping - Stage 1 - Exit Ramp A	1	22-Jul-16	22-Jul-16	14	5d Calendar											Final sweeping - Stage 1 - Exit Ramp A						
A4570	<input type="checkbox"/>	Open ramp - Stage 1 - Exit Ramp A	1	23-Jul-16	23-Jul-16	20	7d Calendar											Open ramp - Stage 1 - Exit Ramp A						
Entrance Ramp B			43	25-May-16	22-Jul-16	15																		
A2230	<input type="checkbox"/>	Break and Remove pavement - Stage 1 - Exit Ramp B	4	25-May-16	30-May-16	19	5d Calendar											Break and Remove pavement - Stage 1 - Exit Ramp B						
A2400	<input type="checkbox"/>	Strip topsoil and ditches - Stage 1 - Exit Ramp B	3	31-May-16	02-Jun-16	19	5d Calendar											Strip topsoil and ditches - Stage 1 - Exit Ramp B						
A2530	<input type="checkbox"/>	Build ditches - Stage 1 - Exit Ramp B	4	03-Jun-16	08-Jun-16	19	5d Calendar											Build ditches - Stage 1 - Exit Ramp B						
A2710	<input type="checkbox"/>	Mass Excavate/Embankment grade - Stage 1 - Exit Ramp B	3	09-Jun-16	13-Jun-16	19	5d Calendar											Mass Excavate/Embankment grade - Stage 1 - Exit Ramp B						
A2850	<input type="checkbox"/>	Complete storm sewer - Stage 1 - Exit Ramp B	3	14-Jun-16	16-Jun-16	19	5d Calendar											Complete storm sewer - Stage 1 - Exit Ramp B						
A2940	<input type="checkbox"/>	Fine grade clay - Stage 1 - Exit Ramp B	2	17-Jun-16	20-Jun-16	19	5d Calendar											Fine grade clay - Stage 1 - Exit Ramp B						
A3030	<input type="checkbox"/>	Place edgedrain - Stage 1 - Exit Ramp B	1	21-Jun-16	21-Jun-16	19	5d Calendar											Place edgedrain - Stage 1 - Exit Ramp B						
A3120	<input type="checkbox"/>	Place fabric and stone - Stage 1 - Exit Ramp B	2	22-Jun-16	23-Jun-16	19	5d Calendar											Place fabric and stone - Stage 1 - Exit Ramp B						
A3220	<input type="checkbox"/>	Trim stone - Stage 1 - Exit Ramp B	1	24-Jun-16	24-Jun-16	19	5d Calendar											Trim stone - Stage 1 - Exit Ramp B						
A3260	<input type="checkbox"/>	Pave Ramp Lanes - Stage 1 - Exit Ramp B	1	28-Jun-16	28-Jun-16	18	5d Calendar											Pave Ramp Lanes - Stage 1 - Exit Ramp B						
A3290	<input type="checkbox"/>	Cure Ramp Lanes - Stage 1 - Exit Ramp B	3	29-Jun-16	01-Jul-16	25	7d Calendar											Cure Ramp Lanes - Stage 1 - Exit Ramp B						
A3460	<input type="checkbox"/>	Trim Outside shoulder - Stage 1 - Exit Ramp B	1	04-Jul-16	04-Jul-16	17	5d Calendar											Trim Outside shoulder - Stage 1 - Exit Ramp B						
A3490	<input type="checkbox"/>	Pave outside shoulder - Stage 1 - Exit Ramp B	1	05-Jul-16	05-Jul-16	17	5d Calendar											Pave outside shoulder - Stage 1 - Exit Ramp B						
A3540	<input type="checkbox"/>	Cure Outside Shoulder - Stage 1 - Exit Ramp B	3	06-Jul-16	08-Jul-16	23	7d Calendar											Cure Outside Shoulder - Stage 1 - Exit Ramp B						
A3730	<input type="checkbox"/>	Fine grade outside slopes - Stage 1 - Exit Ramp B	2	11-Jul-16	12-Jul-16	15	5d Calendar											Fine grade outside slopes - Stage 1 - Exit Ramp B						
A3740	<input type="checkbox"/>	Saw and seal all lanes - Stage 1 - Exit Ramp B	3	11-Jul-16	13-Jul-16	20	5d Calendar											Saw and seal all lanes - Stage 1 - Exit Ramp B						
A3900	<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 1 - Exit Ramp B	3	13-Jul-16	15-Jul-16	15	5d Calendar											Topsoil outside slopes and ditches - Stage 1 - Exit Ramp B						
A4060	<input type="checkbox"/>	Restore outside slopes and ditches - Stage 1 - Exit Ramp B	2	18-Jul-16	19-Jul-16	15	5d Calendar											Restore outside slopes and ditches - Stage 1 - Exit Ramp B						
A4160	<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 1 - Exit Ramp B	1	20-Jul-16	20-Jul-16	15	5d Calendar											Place all signs (Temp and Perm) - Stage 1 - Exit Ramp B						
A4200	<input type="checkbox"/>	Final sweeping - Stage 1 - Exit Ramp B	1	21-Jul-16	21-Jul-16	15	5d Calendar											Final sweeping - Stage 1 - Exit Ramp B						
A4250	<input type="checkbox"/>	Open ramp - Stage 1 - Exit Ramp B	1	22-Jul-16	22-Jul-16	21	7d Calendar											Open ramp - Stage 1 - Exit Ramp B						
2016 Roadwork - Stage 2			64	30-Jul-16	29-Oct-16	11																		
A7080	<input checked="" type="checkbox"/>	Switch Traffic	2	30-Jul-16	31-Jul-16	4	Weekend only												Switch Traffic					
SB Reconstruct (POE to Sta 2258+00)			63	01-Aug-16	27-Oct-16	11																		
A6560																								

Remaining Level of Effort

Actual Work

Critical Remaining Work

WBS Summary Activity

Actual Level of Effort

Remaining Work

Milestone

WBS Summary Progress



10576-190706 I-75 Reconstruction - Wayne County

Road Reconstruction Baseline Schedule Example

Data Date: 1/12/16

Run Date: 1/25/16

Submission Date: 1/27/16

Contractor: ABC Construction, Inc.

Activity ID	Longest Path	Activity Name	Original Duration	Start	Finish	Total Float	Calendar	2016												2017		
								Dec	Jan		Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
A6420	<input checked="" type="checkbox"/>	Place edgedrain - Stage 2 - POE to Sta 2258+00	4	13-Sep-16	16-Sep-16	10	5d Calendar										Place edgedrain - Stage 2 - POE to Sta 2258+00					
A6400	<input checked="" type="checkbox"/>	Trim stone - Stage 2 - POE to Sta 2258+00	4	19-Sep-16	22-Sep-16	10	5d Calendar										Trim stone - Stage 2 - POE to Sta 2258+00					
A6390	<input checked="" type="checkbox"/>	Pave 24' lane - Stage 2 - POE to Sta 2258+00	1	23-Sep-16	23-Sep-16	10	5d Calendar										Pave 24' lane - Stage 2 - POE to Sta 2258+00					
A6380	<input checked="" type="checkbox"/>	Cure 24' lane - Stage 2 - POE to Sta 2258+00	3	24-Sep-16	26-Sep-16	15	7d Calendar										Cure 24' lane - Stage 2 - POE to Sta 2258+00					
A6340	<input type="checkbox"/>	Pave outside shoulder - Stage 2 - POE to Sta 2258+00	1	27-Sep-16	27-Sep-16	13	5d Calendar										Pave outside shoulder - Stage 2 - POE to Sta 2258+00					
A6370	<input checked="" type="checkbox"/>	Trim 2nd 24' lane - Stage 2 - POE to Sta 2258+00	2	27-Sep-16	28-Sep-16	11	5d Calendar										Trim 2nd 24' lane - Stage 2 - POE to Sta 2258+00					
A6330	<input type="checkbox"/>	Cure on outside shoulder - Stage 2 - POE to Sta 2258+00	2	28-Sep-16	29-Sep-16	19	7d Calendar										Cure on outside shoulder - Stage 2 - POE to Sta 2258+00					
A6360	<input checked="" type="checkbox"/>	Pave 2nd 24' lane - Stage 2 - POE to Sta 2258+00	1	29-Sep-16	29-Sep-16	11	5d Calendar										Pave 2nd 24' lane - Stage 2 - POE to Sta 2258+00					
A6350	<input checked="" type="checkbox"/>	Cure 2nd 24' lane - Stage 2 - POE to Sta 2258+00	3	30-Sep-16	02-Oct-16	16	7d Calendar										Cure 2nd 24' lane - Stage 2 - POE to Sta 2258+00					
A6570	<input type="checkbox"/>	Fine grade outside slopes - Stage 2 - POE to Sta 2258+00	2	30-Sep-16	03-Oct-16	18	5d Calendar										Fine grade outside slopes - Stage 2 - POE to Sta 2258+00					
A6620	<input checked="" type="checkbox"/>	Cleanup inside shoulder - Stage 2 - POE to Sta 2258+00	1	03-Oct-16	03-Oct-16	12	5d Calendar										Cleanup inside shoulder - Stage 2 - POE to Sta 2258+00					
A6550	<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 2 - POE to Sta 2258+00	2	04-Oct-16	05-Oct-16	18	5d Calendar										Topsoil outside slopes and ditches - Stage 2 - POE to Sta 2258+00					
A6610	<input checked="" type="checkbox"/>	Pave inside shoulder - Stage 2 - POE to Sta 2258+00	1	04-Oct-16	04-Oct-16	12	5d Calendar										Pave inside shoulder - Stage 2 - POE to Sta 2258+00					
A6600	<input checked="" type="checkbox"/>	Cure on inside shoulder - Stage 2 - POE to Sta 2258+00	3	05-Oct-16	07-Oct-16	16	7d Calendar										Cure on inside shoulder - Stage 2 - POE to Sta 2258+00					
A6540	<input type="checkbox"/>	Restore outside slopes and ditches - Stage 2 - POE to Sta 2258+00	2	06-Oct-16	07-Oct-16	18	5d Calendar										Restore outside slopes and ditches - Stage 2 - POE to Sta 2258+00					
A6530	<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 2 - POE to Sta 2258+00	5	10-Oct-16	14-Oct-16	18	5d Calendar										Place all signs (Temp and Perm) - Stage 2 - POE to Sta 2258+00					
A6590	<input checked="" type="checkbox"/>	Place median drainage (VG or Ditches) - Stage 2 - POE to Sta 2258+00	3	10-Oct-16	12-Oct-16	10	5d Calendar										Place median drainage (VG or Ditches) - Stage 2 - POE to Sta 2258+00					
A6580	<input checked="" type="checkbox"/>	Place median barrier wall where applicable - Stage 2 - POE to Sta 2258+00	5	13-Oct-16	19-Oct-16	10	5d Calendar										Place median barrier wall where applicable - Stage 2 - POE to Sta 2258+00					
A6520	<input checked="" type="checkbox"/>	Run ride quality on all lanes - Stage 2 - POE to Sta 2258+00	2	20-Oct-16	21-Oct-16	10	5d Calendar										Run ride quality on all lanes - Stage 2 - POE to Sta 2258+00					
A6510	<input checked="" type="checkbox"/>	Grind as needed on lanes - Stage 2 - POE to Sta 2258+00	2	24-Oct-16	25-Oct-16	10	5d Calendar										Grind as needed on lanes - Stage 2 - POE to Sta 2258+00					
A6490	<input type="checkbox"/>	Cleanup / Striping - Stage 2 - POE to Sta 2258+00	2	26-Oct-16	27-Oct-16	11	5d Calendar										Cleanup / Striping - Stage 2 - POE to Sta 2258+00					
A6500	<input type="checkbox"/>	Saw and seal all lanes - Stage 2 - POE to Sta 2258+00	2	26-Oct-16	27-Oct-16	11	5d Calendar										Saw and seal all lanes - Stage 2 - POE to Sta 2258+00					
SB Reconstruct (Sta 2175+00 to POB)			55	12-Aug-16	29-Oct-16	11																
A6320	<input checked="" type="checkbox"/>	Break and Remove pavement - Stage 2 - Sta 2175+00 to POB	8	12-Aug-16	23-Aug-16	15	5d Calendar										Break and Remove pavement - Stage 2 - Sta 2175+00 to POB					
A6290	<input type="checkbox"/>	Mass Excavate/Embankment grade - Stage 2 - Sta 2175+00 to POB	5	24-Aug-16	30-Aug-16	15	5d Calendar										Mass Excavate/Embankment grade - Stage 2 - Sta 2175+00 to POB					
A6300	<input type="checkbox"/>	Build ditches - Stage 2 - Sta 2175+00 to POB	5	24-Aug-16	30-Aug-16	15	5d Calendar										Build ditches - Stage 2 - Sta 2175+00 to POB					
A6310	<input type="checkbox"/>	Strip topsoil and ditches - Stage 2 - Sta 2175+00 to POB	5	24-Aug-16	30-Aug-16	15	5d Calendar										Strip topsoil and ditches - Stage 2 - Sta 2175+00 to POB					
A6280	<input type="checkbox"/>	Complete storm sewer - Stage 2 - Sta 2175+00 to POB	5	31-Aug-16	07-Sep-16	15	5d Calendar										Complete storm sewer - Stage 2 - Sta 2175+00 to POB					
A6260	<input type="checkbox"/>	Place edgedrain - Stage 2 - Sta 2175+00 to POB	5	08-Sep-16	14-Sep-16	15	5d Calendar										Place edgedrain - Stage 2 - Sta 2175+00 to POB					
A6270	<input type="checkbox"/>	Fine grade clay - Stage 2 - Sta 2175+00 to POB	5	08-Sep-16	14-Sep-16	15	5d Calendar										Fine grade clay - Stage 2 - Sta 2175+00 to POB					
A6250	<input type="checkbox"/>	Place fabric and stone - Stage 2 - Sta 2175+00 to POB	4	15-Sep-16	20-Sep-16	15	5d Calendar										Place fabric and stone - Stage 2 - Sta 2175+00 to POB					
A6240	<input type="checkbox"/>	Trim stone - Stage 2 - Sta 2175+00 to POB	2	21-Sep-16	22-Sep-16	15	5d Calendar										Trim stone - Stage 2 - Sta 2175+00 to POB					
A6230	<input type="checkbox"/>	Pave 24' lane - Stage 2 - Sta 2175+00 to POB	1	26-Sep-16	26-Sep-16	14	5d Calendar										Pave 24' lane - Stage 2 - Sta 2175+00 to POB					
A6220	<input type="checkbox"/>	Cure 24' lane - Stage 2 - Sta 2175+00 to POB	3	27-Sep-16	29-Sep-16	19	7d Calendar										Cure 24' lane - Stage 2 - Sta 2175+00 to POB					
A6180	<input type="checkbox"/>	Clean up outside shoulder for paving - Stage 2 - Sta 2175+00 to POB	1	30-Sep-16	30-Sep-16	15	5d Calendar										Clean up outside shoulder for paving - Stage 2 - Sta 2175+00 to POB					
A6210	<input type="checkbox"/>	Trim 2nd 24' lane - Stage 2 - Sta 2175+00 to POB	2	30-Sep-16	03-Oct-16	13	5d Calendar										Trim 2nd 24' lane - Stage 2 - Sta 2175+00 to POB					
A6170	<input type="checkbox"/>	Pave outside shoulder - Stage 2 - Sta 2175+00 to POB	1	03-Oct-16	03-Oct-16	15	5d Calendar										Pave outside shoulder - Stage 2 - Sta 2175+00 to POB					
A6160	<input type="checkbox"/>	Cure on outside shoulder - Stage 2 - Sta 2175+00 to POB	2	04-Oct-16	05-Oct-16	21	7d Calendar										Cure on outside shoulder - Stage 2 - Sta 2175+00 to POB					
A6200	<input type="checkbox"/>	Pave 2nd 24' lane - Stage 2 - Sta 2175+00 to POB	1	04-Oct-16	04-Oct-16	13	5d Calendar										Pave 2nd 24' lane - Stage 2 - Sta 2175+00 to POB					
A6190	<input type="checkbox"/>	Cure 2nd 24' lane - Stage 2 - Sta 2175+00 to POB	3	05-Oct-16	07-Oct-16	19	7d Calendar										Cure 2nd 24' lane - Stage 2 - Sta 2175+00 to POB					
A6090	<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 2 - Sta 2175+00 to POB	2	06-Oct-16	07-Oct-16	17	5d Calendar										Topsoil outside slopes and ditches - Stage 2 - Sta 2175+00 to POB					
A6100	<input type="checkbox"/>	Fine grade outside slopes - Stage 2 - Sta 2175+00 to POB	2	06-Oct-16	07-Oct-16	17	5d Calendar										Fine grade outside slopes - Stage 2 - Sta 2175+00 to POB					
A6080	<input type="checkbox"/>	Restore outside slopes and ditches - Stage 2 - Sta 2175+00 to POB	2	10-Oct-16	11-Oct-16	17	5d Calendar										Restore outside slopes and ditches - Stage 2 - Sta 2175+00 to POB					
A6150	<input type="checkbox"/>	Cleanup inside shoulder - Stage 2 - Sta 2175+00 to POB	1	10-Oct-16	10-Oct-16	13	5d Calendar										Cleanup inside shoulder - Stage 2 - Sta 2175+00 to POB					
A6140	<input type="checkbox"/>	Pave inside shoulder - Stage 2 - Sta 2175+00 to POB	1	11-Oct-16	11-Oct-16	13	5d Calendar															

Remaining Level of Effort Actual Work Critical Remaining Work WBS Summary Activity
 Actual Level of Effort Remaining Work Milestone WBS Summary Progress



10576-190706 I-75 Reconstruction - Wayne County

Road Reconstruction Baseline Schedule Example

Data Date: 1/12/16

Run Date: 1/25/16

Submission Date: 1/27/16

Contractor: ABC Construction, Inc.

Activity ID	Longest Path	Activity Name	Original Duration	Start	Finish	Total Float	Calendar	2016												2017		
								Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
A6980	<input type="checkbox"/>	Trim stone - Stage 2 - Exit Ramp C	2	14-Sep-16	15-Sep-16	25	5d Calendar										<input type="checkbox"/>	Trim stone - Stage 2 - Exit Ramp C				
A6970	<input type="checkbox"/>	Pave Ramp Lanes - Stage 2 - Exit Ramp C	1	30-Sep-16	30-Sep-16	15	5d Calendar										<input type="checkbox"/>	Pave Ramp Lanes - Stage 2 - Exit Ramp C				
A6960	<input type="checkbox"/>	Cure Ramp Lanes - Stage 2 - Exit Ramp C	3	01-Oct-16	03-Oct-16	22	7d Calendar										<input type="checkbox"/>	Cure Ramp Lanes - Stage 2 - Exit Ramp C				
A6950	<input type="checkbox"/>	Trim Outside shoulder - Stage 2 - Exit Ramp C	1	04-Oct-16	04-Oct-16	16	5d Calendar										<input type="checkbox"/>	Trim Outside shoulder - Stage 2 - Exit Ramp C				
A6850	<input type="checkbox"/>	Pave outside shoulder - Stage 2 - Exit Ramp C	1	05-Oct-16	05-Oct-16	16	5d Calendar										<input type="checkbox"/>	Pave outside shoulder - Stage 2 - Exit Ramp C				
A6940	<input type="checkbox"/>	Cure Outside Shoulder - Stage 2 - Exit Ramp C	3	06-Oct-16	08-Oct-16	22	7d Calendar										<input type="checkbox"/>	Cure Outside Shoulder - Stage 2 - Exit Ramp C				
A6890	<input type="checkbox"/>	Saw and seal all lanes - Stage 2 - Exit Ramp C	2	10-Oct-16	11-Oct-16	22	5d Calendar										<input type="checkbox"/>	Saw and seal all lanes - Stage 2 - Exit Ramp C				
A6930	<input type="checkbox"/>	Fine grade outside slopes - Stage 2 - Exit Ramp C	3	10-Oct-16	12-Oct-16	15	5d Calendar										<input type="checkbox"/>	Fine grade outside slopes - Stage 2 - Exit Ramp C				
A6920	<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 2 - Exit Ramp C	3	13-Oct-16	17-Oct-16	15	5d Calendar										<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 2 - Exit Ramp C				
A6910	<input type="checkbox"/>	Restore outside slopes and ditches - Stage 2 - Exit Ramp C	2	18-Oct-16	19-Oct-16	15	5d Calendar										<input type="checkbox"/>	Restore outside slopes and ditches - Stage 2 - Exit Ramp C				
A6900	<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 2 - Exit Ramp C	1	20-Oct-16	20-Oct-16	15	5d Calendar										<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 2 - Exit Ramp C				
A6880	<input type="checkbox"/>	Final sweeping - Stage 2 - Exit Ramp C	1	21-Oct-16	21-Oct-16	15	5d Calendar										<input type="checkbox"/>	Final sweeping - Stage 2 - Exit Ramp C				
A6860	<input type="checkbox"/>	Open ramp - Stage 2 - Exit Ramp C	1	22-Oct-16	22-Oct-16	23	7d Calendar										<input type="checkbox"/>	Open ramp - Stage 2 - Exit Ramp C				
Entrance Ramp D			42	24-Aug-16	21-Oct-16	16																
A6790	<input type="checkbox"/>	Break and Remove pavement - Stage 2 - Exit Ramp D	4	24-Aug-16	29-Aug-16	18	5d Calendar										<input type="checkbox"/>	Break and Remove pavement - Stage 2 - Exit Ramp D				
A6780	<input type="checkbox"/>	Strip topsoil and ditches - Stage 2 - Exit Ramp D	3	30-Aug-16	01-Sep-16	18	5d Calendar										<input type="checkbox"/>	Strip topsoil and ditches - Stage 2 - Exit Ramp D				
A6770	<input type="checkbox"/>	Build ditches - Stage 2 - Exit Ramp D	4	02-Sep-16	08-Sep-16	18	5d Calendar										<input type="checkbox"/>	Build ditches - Stage 2 - Exit Ramp D				
A6760	<input type="checkbox"/>	Mass Excavate/Embankment grade - Stage 2 - Exit Ramp D	3	09-Sep-16	13-Sep-16	18	5d Calendar										<input type="checkbox"/>	Mass Excavate/Embankment grade - Stage 2 - Exit Ramp D				
A6750	<input type="checkbox"/>	Complete storm sewer - Stage 2 - Exit Ramp D	3	14-Sep-16	16-Sep-16	18	5d Calendar										<input type="checkbox"/>	Complete storm sewer - Stage 2 - Exit Ramp D				
A6740	<input type="checkbox"/>	Fine grade clay - Stage 2 - Exit Ramp D	2	19-Sep-16	20-Sep-16	18	5d Calendar										<input type="checkbox"/>	Fine grade clay - Stage 2 - Exit Ramp D				
A6730	<input type="checkbox"/>	Place edgedrain - Stage 2 - Exit Ramp D	1	21-Sep-16	21-Sep-16	18	5d Calendar										<input type="checkbox"/>	Place edgedrain - Stage 2 - Exit Ramp D				
A6830	<input type="checkbox"/>	Place fabric and stone - Stage 2 - Exit Ramp D	2	22-Sep-16	23-Sep-16	18	5d Calendar										<input type="checkbox"/>	Place fabric and stone - Stage 2 - Exit Ramp D				
A6720	<input type="checkbox"/>	Trim stone - Stage 2 - Exit Ramp D	1	26-Sep-16	26-Sep-16	18	5d Calendar										<input type="checkbox"/>	Trim stone - Stage 2 - Exit Ramp D				
A6710	<input type="checkbox"/>	Pave Ramp Lanes - Stage 2 - Exit Ramp D	1	30-Sep-16	30-Sep-16	15	5d Calendar										<input type="checkbox"/>	Pave Ramp Lanes - Stage 2 - Exit Ramp D				
A6700	<input type="checkbox"/>	Cure Ramp Lanes - Stage 2 - Exit Ramp D	3	01-Oct-16	03-Oct-16	23	7d Calendar										<input type="checkbox"/>	Cure Ramp Lanes - Stage 2 - Exit Ramp D				
A6690	<input type="checkbox"/>	Trim Outside shoulder - Stage 2 - Exit Ramp D	1	04-Oct-16	04-Oct-16	17	5d Calendar										<input type="checkbox"/>	Trim Outside shoulder - Stage 2 - Exit Ramp D				
A6680	<input type="checkbox"/>	Pave outside shoulder - Stage 2 - Exit Ramp D	1	05-Oct-16	05-Oct-16	17	5d Calendar										<input type="checkbox"/>	Pave outside shoulder - Stage 2 - Exit Ramp D				
A6670	<input type="checkbox"/>	Cure Outside Shoulder - Stage 2 - Exit Ramp D	3	06-Oct-16	08-Oct-16	23	7d Calendar										<input type="checkbox"/>	Cure Outside Shoulder - Stage 2 - Exit Ramp D				
A6660	<input type="checkbox"/>	Fine grade outside slopes - Stage 2 - Exit Ramp D	2	10-Oct-16	11-Oct-16	16	5d Calendar										<input type="checkbox"/>	Fine grade outside slopes - Stage 2 - Exit Ramp D				
A6840	<input type="checkbox"/>	Saw and seal all lanes - Stage 2 - Exit Ramp D	3	10-Oct-16	12-Oct-16	21	5d Calendar										<input type="checkbox"/>	Saw and seal all lanes - Stage 2 - Exit Ramp D				
A6650	<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 2 - Exit Ramp D	3	12-Oct-16	14-Oct-16	16	5d Calendar										<input type="checkbox"/>	Topsoil outside slopes and ditches - Stage 2 - Exit Ramp D				
A6640	<input type="checkbox"/>	Restore outside slopes and ditches - Stage 2 - Exit Ramp D	2	17-Oct-16	18-Oct-16	16	5d Calendar										<input type="checkbox"/>	Restore outside slopes and ditches - Stage 2 - Exit Ramp D				
A6630	<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 2 - Exit Ramp D	1	19-Oct-16	19-Oct-16	16	5d Calendar										<input type="checkbox"/>	Place all signs (Temp and Perm) - Stage 2 - Exit Ramp D				
A6800	<input type="checkbox"/>	Final sweeping - Stage 1 - Stage 2 - Exit Ramp D	1	20-Oct-16	20-Oct-16	16	5d Calendar										<input type="checkbox"/>	Final sweeping - Stage 1 - Stage 2 - Exit Ramp D				
A6810	<input type="checkbox"/>	Open ramp - Stage 1 - Stage 2 - Exit Ramp D	1	21-Oct-16	21-Oct-16	24	7d Calendar										<input type="checkbox"/>	Open ramp - Stage 1 - Stage 2 - Exit Ramp D				

Page 5 of 5
