Analysis: Profilograph Simulation

Inputs

Blanking Band (in): 0.2
Minimum Scallop Width (ft): 2.00
Minimum Scallop Height (in): 0.0
Scallop Rounding Increment (in): 0.1
Segment Length (ft): 528.00
Rounded Profile Index: Yes

Wheel Offsets

Name	Value (ft)
Offset 1	8.75
Offset 2	11.25
Offset 3	13.75
Offset 4	16.25
Offset 5	11.25
Offset 6	13.75

Selections

File	Profile	Basis	Section	Filter
run4R	LElev.	Yes	Full	Butterworth Low-pass (1.97 ft)

Simulation Results

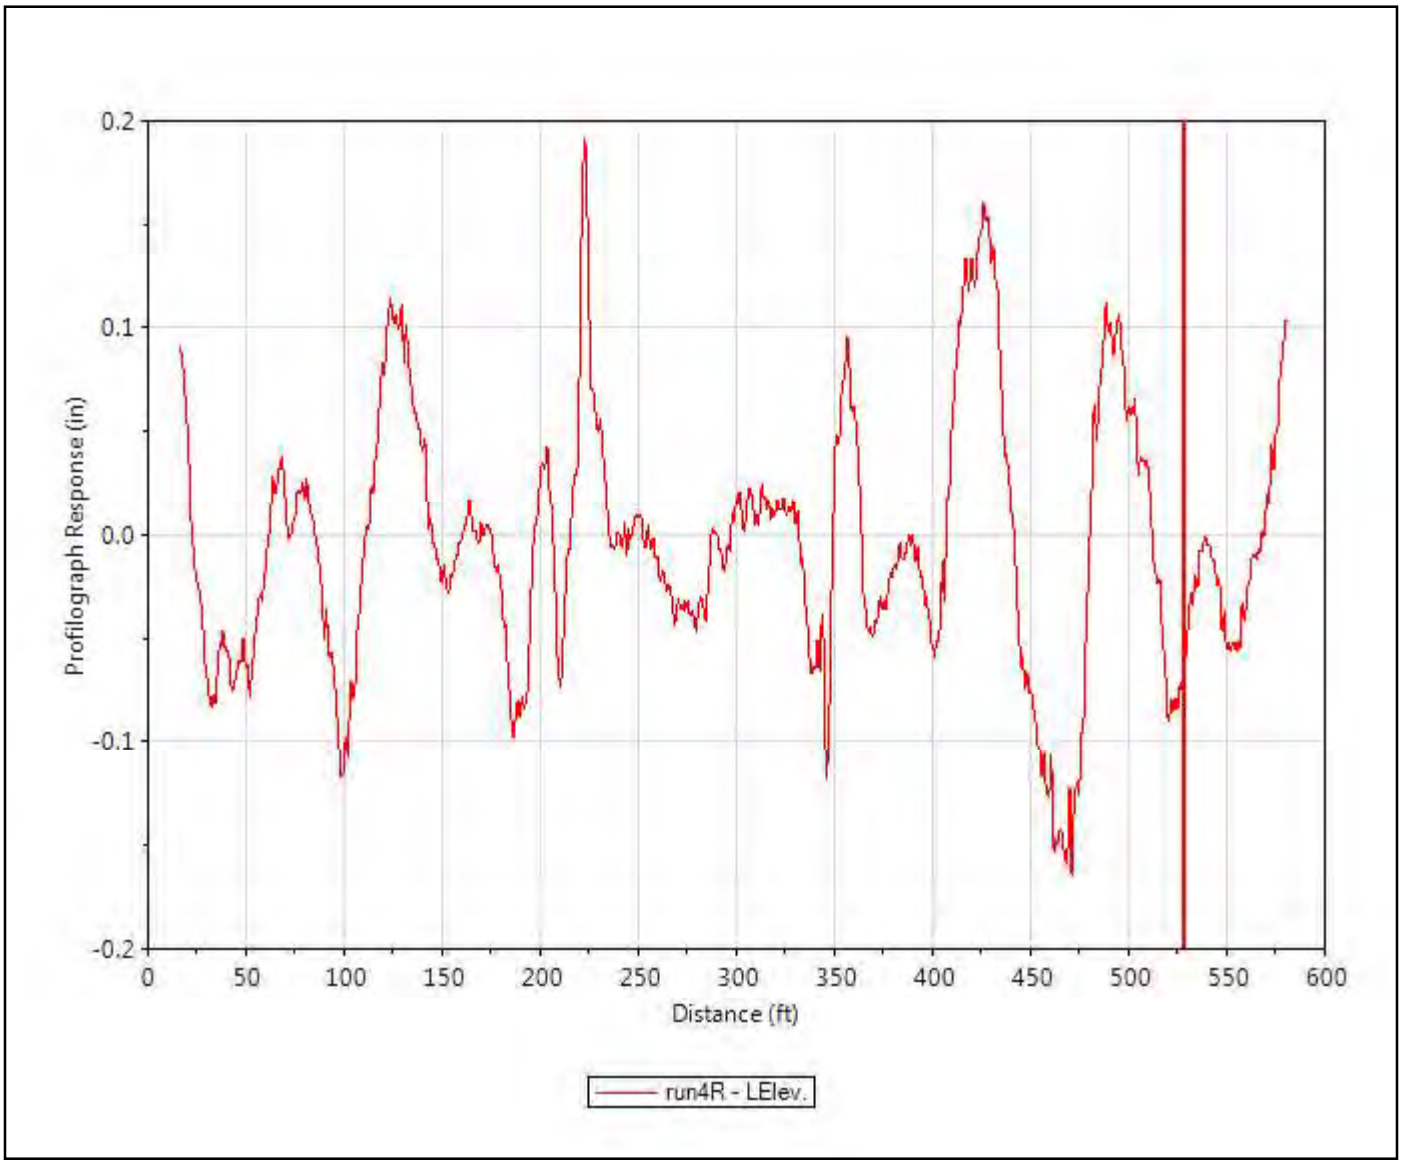

Start Distance (ft)	Stop Distance (ft)	run4R - LElev.
16.43	527.94	2.06
528.17	580.44	0.00

Scallops: run4R - LElev.

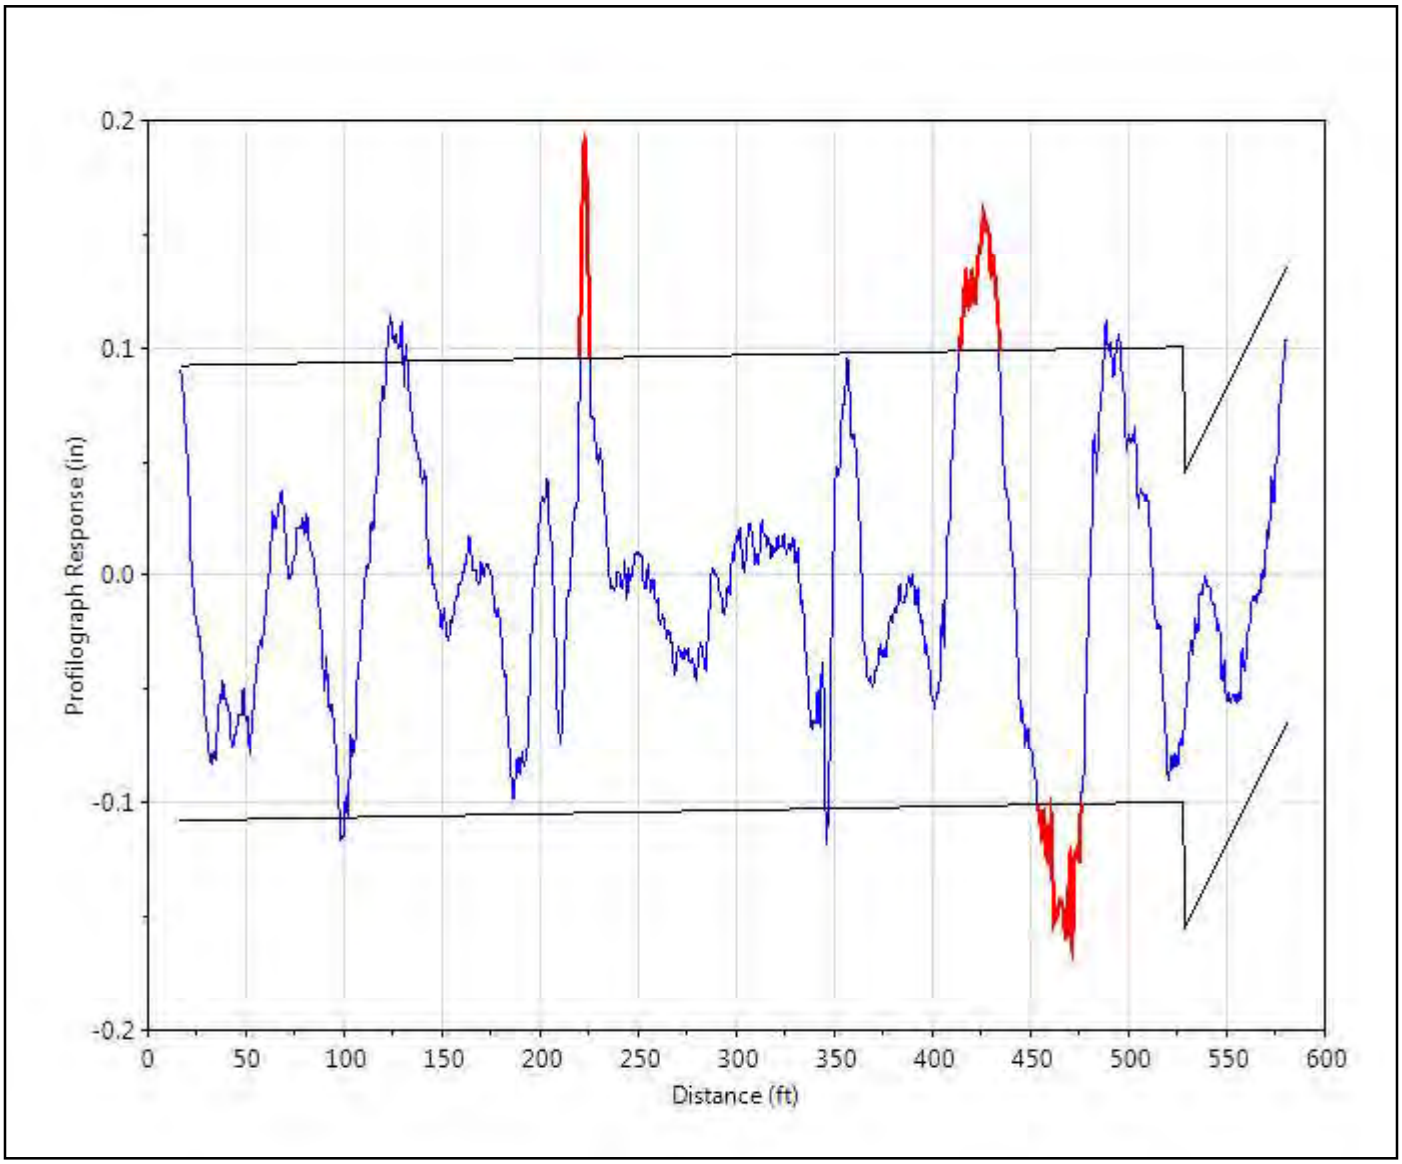

Scallop	Start Distance (ft)	Stop Distance (ft)	Height (in)
Up	220.15	225.09	0.10
Up	413.19	433.98	0.05
Down	453.57	475.63	0.05
