Appendix B: Facility Conditions Index Report

DRAFT

Combined Condition Assessment

Robert Burns Elementary

14350 Terry Street, Detroit, Michigan

February 2017

DTMB
Technology, Management & Budget
State Facilities Administration

SRO
STATE SCHOOL REFORM/REDESIGN OFFICE
Michigan Department of Technology, Management and Budget

LARA
LICENSING AND REGULATORY AFFAIRS
CUSTOMER DRIVEN. BUSINESS MINDED
Bureau of Construction Codes

Executive Summary

This Combined Condition Assessment is the product of a collaborative site assessment and survey by the Department of Technology Management and Budget, State Facilities Administration (SFA) and the Department of Licensing and Regulatory Affairs (LARA) Bureau of Construction Codes at the request of the State School Reform/Redesign Office (SRO).

It has been designed to provide a general condition overview of the facility and major site assets. A team visits the site and collects data to determine two factors in eight facilities categories:

Factors:

- ***Remaining Service Life*** of Facility Elements or Systems which is then utilized to calculate an ***Age-Based Condition Index***.
- ***Operating Condition*** based upon visual observations the day of the visit along with supporting information/records provided by staff or contact personnel.
- Results of the two factors above are averaged/combined to produce a single ***Combined Condition Score (CCS)*** for the site.

Facilities Categories:

- Structure – Foundation, Parking Lots, Sidewalks, Access
- Exterior – Walls, Windows, Stairways, Doors
- Roofing – Roofing Type and Condition
- HVAC – Air Handlers, Boilers, Chillers, Gas Piping, Cooling Towers, Pumps, Exhaust, etc.
- Electrical – Service & Distribution, Lighting, Emergency Generator, Fire Alarm, Kitchen
- Plumbing – Restrooms, Backflow, Domestic Water/Heating, Distribution, Fire System
- Conveying – Elevators, Lifts
- Interior Construction – Doors, Stairways, Walls, Ceilings, Flooring

Results:

The Robert Burns Elementary assessment was performed on ***February 9, 2017*** by the LARA team and resulted in a ***CCS*** of: **47.5**

Combined Condition Score (CCS)

There are many ways to measure physical condition of a facility. Performing full, detailed assessments necessary to calculate a Facility Condition Index (FCI), Extended Facility Condition Index (EFCI) or Facilities Needs Index (FNI) are very demanding in terms of input resources up front. This project required an efficient, lean approach whereby an assessment team could move through occupied space quickly with minimal disruption while collecting data. The output needed to be measurable and consistent. While additional information such as annual

DRAFT

reinvestment rates and replacement costs may also be desirable, these were outside the scope of this first visit.

The DTMB State Facilities Administration (SFA), Building Operations Division assesses buildings within their own portfolio for capital planning purposes. These assessments may be age-based, where the age of building elements or assets are compared to their respective design-life; or observed-condition-based where defects and site conditions are observed and rated.

The Combined Condition Score is a combination of both the age-based condition index and observed condition, equally weighted and averaged together resulting in a number between 0 and 100. This number will be indicative of overall facility condition and can be used to order facilities by respective condition relative to others.

- A score of 100 indicates a brand new, unoccupied facility with no construction defects and no code violations.
- A score of 0 indicates a very old facility with no usable architectural elements or attached assets.
- Realistically speaking, all occupied buildings will score more than zero and less than 100.
- The lower the score, the less cost effective to operate the building. A good rule-of-thumb is when the score falls below 34, equivalent annual cost to replace a facility will be less than continuing to operate and maintain the existing facility.

DRAFT

Building Exterior

Roof and New Addition Roof-Top Units

Interior Water Damage

Site Narrative

The assessment team completed the site visit/inspection on February 9, 2017. The Team reviewed the exterior of the building including roofing, exterior walls, generator and outdoor mechanicals. The team then moved inside and reviewed interior finishes and mechanicals including but not limited to, walls and ceilings, foundations, boiler heating, plumbing, HVAC systems and electrical systems in the building. The following was validated/noted during the inspection with site personnel:

- The site was originally constructed in 1923.
- Some water intrusion damage was noted during the site visit.
- Major renovations and a new addition were completed since original construction.
- No information regarding when work was done or scope of work was available.

The full Combined Condition Assessment is as follows:

DRAFT

BUILDING NAME: Burns Elementary-Middle School

BUILT: 6/1/1923

ASSESSMENT DATE: 2/9/2017

CATEGORY	SUB-CATEGORY	TYPE	INSTALLED DATE	(YEARS) SERVICE LIFE	AGE	REMAINING SERVICE LIFE	AGE-BASED CONDITION INDEX	INSPECTED OPERATING CONDITION	COMMENTS
STRUCTURE						-8.1	5.8	75.0	
	FOUNDATION		6/1/1923	75.0	93.7	-18.7	0.0	75.0	
	PARKING LOTS		6/1/1994	15.0	22.7	-7.7	0.0	75.0	
	PEDESTRIAN PAVING		6/1/1994	25.0	22.7	2.3	17.3	75.0	
EXTERIOR						22.3	63.3	75.0	
	WALLS		6/1/1994	70.0	22.7	47.3	89.5	75.0	
	WINDOWS		6/1/1994	30.0	22.7	7.3	42.6	75.0	
	STAIRWAYS								
	DOORS		6/1/1994	35.0	22.7	12.3	57.8	75.0	
ROOF						-2.7	0.0	71.4	
	ROOF COVERING		6/1/1994	20.0	22.7	-2.7	0.0	71.4	
HVAC						8.1	22.2	56.4	
	AIR HANDLING UNITS		6/1/1994	20.0	22.7	-2.7	0.0	53.1	
	BOILERS		6/1/1994	30.0	22.7	7.3	42.6	50.0	
	CHILLERS								
	GAS PIPING SYSTEMS		6/1/1994	75.0	22.7	52.3	90.8	50.0	
	COOLING TOWERS								
	PUMPS		6/1/1994	20.0	22.7	-2.7	0.0	50.0	
	EXHAUST SYSTEMS		6/1/1994	20.0	22.7	-2.7	0.0	60.0	
	WALK IN FREEZERS		6/1/1994	20.0	22.7	-2.7	0.0	75.0	
	VENT AND POOL HEATERS								
	COOLING PIPING								
ELECTRICAL						-2.7	33.6	55.6	
	ELECTRICAL SERVICE/DISTRIBUTION		6/1/1994	50.0	22.7	27.3	79.3	53.1	
	LIGHTING		6/1/1994	20.0	22.7	-2.7	0.0	50.0	
	EMERGENCY GENERATOR								
	KITCHEN EQUIPMENT		6/1/2010	20.0	6.7	13.3	88.7	75.0	
	INTERCOM / PA EQUIPMENT		6/1/1994	20.0	22.7	-2.7	0.0	50.0	
	FIRE ALARM SYSTEM		6/1/1994	20.0	22.7	-2.7	0.0	50.0	
PLUMBING						7.3	50.7	57.3	
	RESTROOMS		6/1/1994	30.0	22.7	7.3	42.6	50.2	
	BACKFLOW PREVENTERS		6/1/1994	10.0	22.7	-12.7	0.0	50.0	
	GENERAL		6/1/1994	35.0	22.7	12.3	57.8	55.0	
	FOOD SERVICE		6/1/2010	35.0	6.7	28.3	95.3	75.0	
	DOMESTIC WATER HEATING		6/1/1994	15.0	22.7	-7.7	0.0	66.7	
	WATER DISTRIBUTION		6/1/1994	75.0	22.7	52.3	90.8	50.0	
	FIRE SUPPRESSION		6/1/1994	40.0	22.7	17.3	67.7	50.0	
CONVEYING									
	ELEVATORS								
INTERIOR CONSTRUCTION						24.3	63.4	65.0	
	DOORS		6/1/1994	40.0	22.7	17.3	67.7	50.0	
	STAIRWAYS		6/1/1994	50.0	22.7	27.3	79.3	50.0	
	WALLS		6/1/1994	75.0	22.7	52.3	90.8	75.0	
	CEILINGS		6/1/1994	20.0	22.7	-2.7	0.0	75.0	
	FLOORS		6/1/1994	50.0	22.7	27.3	79.3	75.0	

BUILDING EXTERIOR FT^2
63,370

AVERAGE					COMBINED CONDITION SCORE
SERVICE LIFE	AGE	REMAINING SERVICE LIFE	CONDITION INDEX	OBSERVED CONDITION	47.5
35.3	24.0	6.9	33.5	61.5	

DRAFT

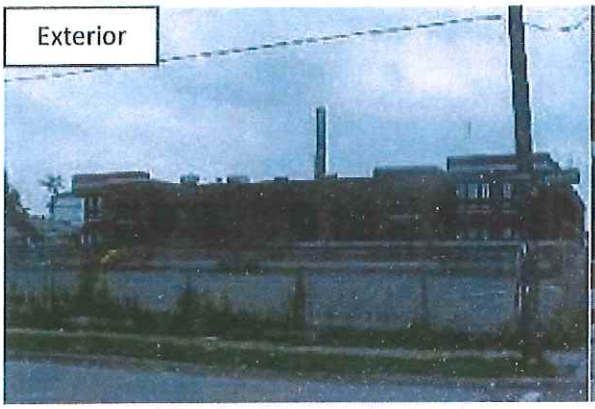

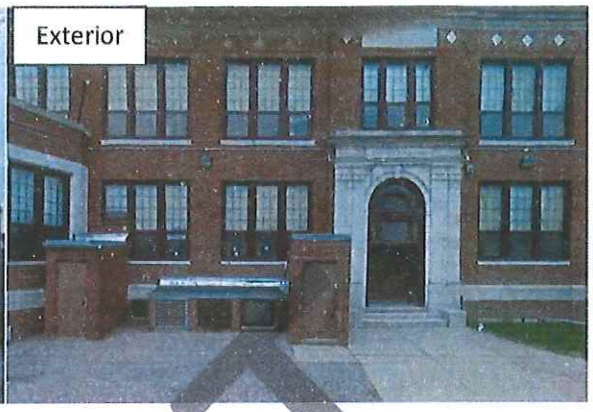

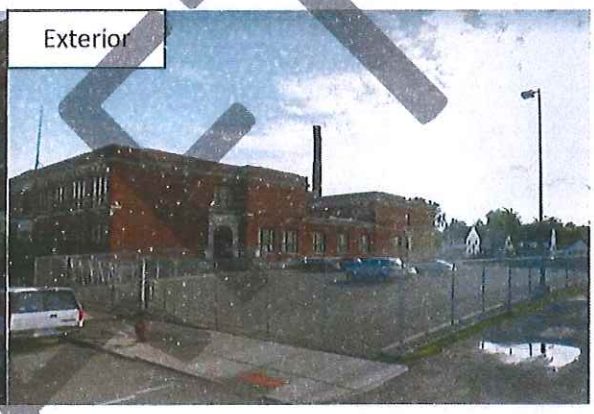

DRAFT

Fire Inspection

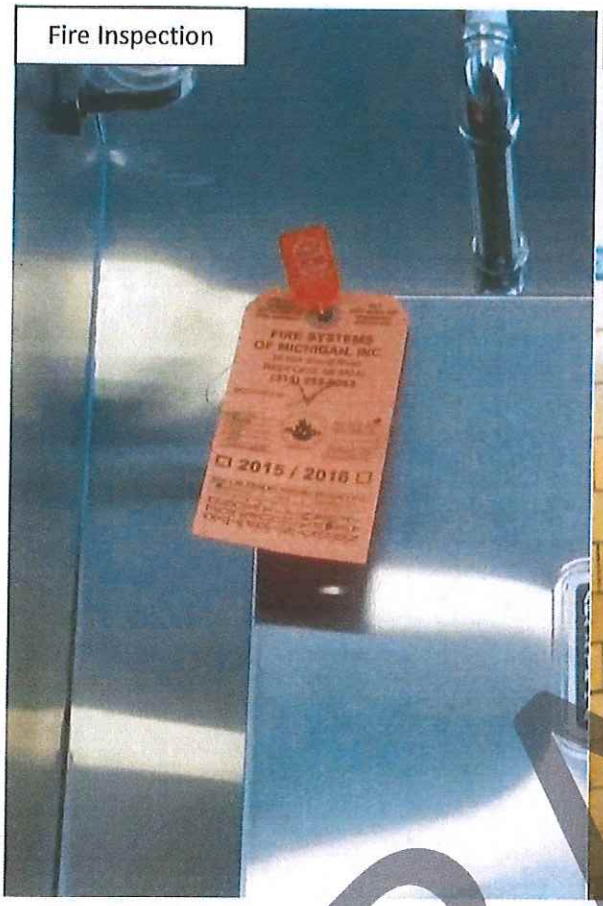

Bathroom Entrance

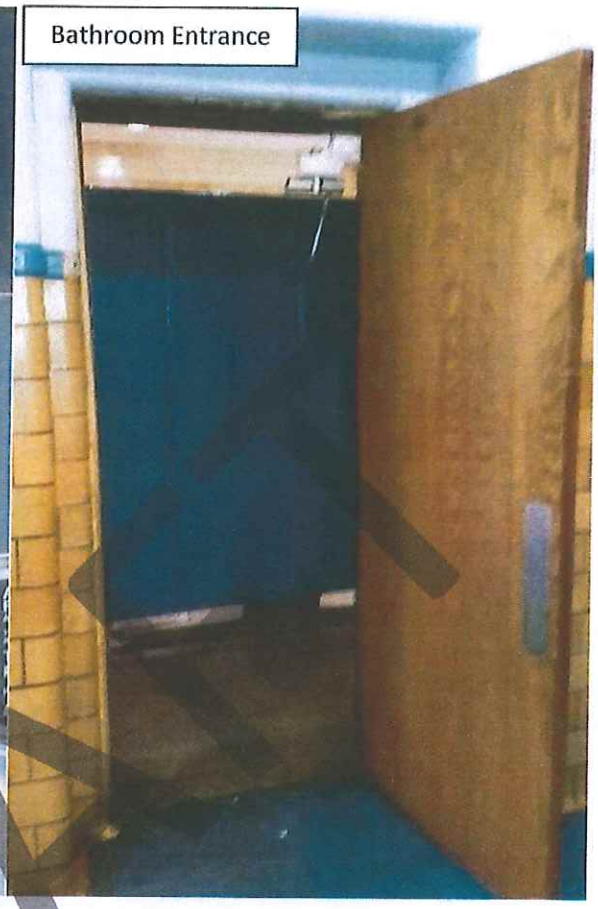

DRAFT

Lower Roof

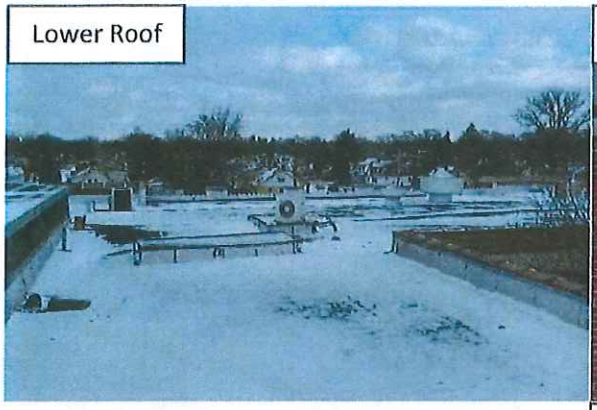

Exterior

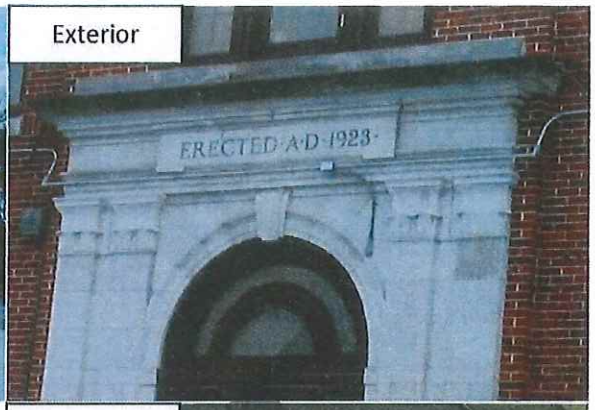

Roof Leak

Roof

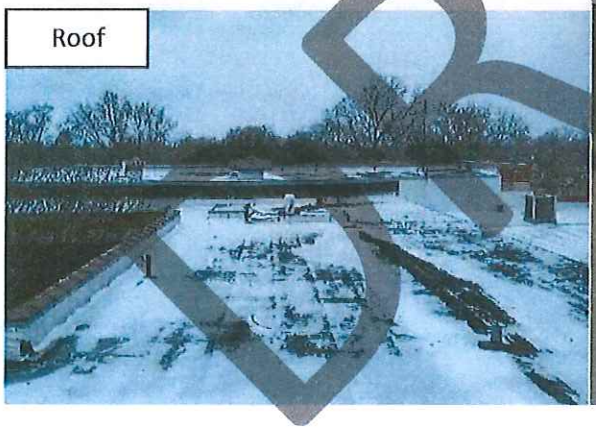

DRAFT

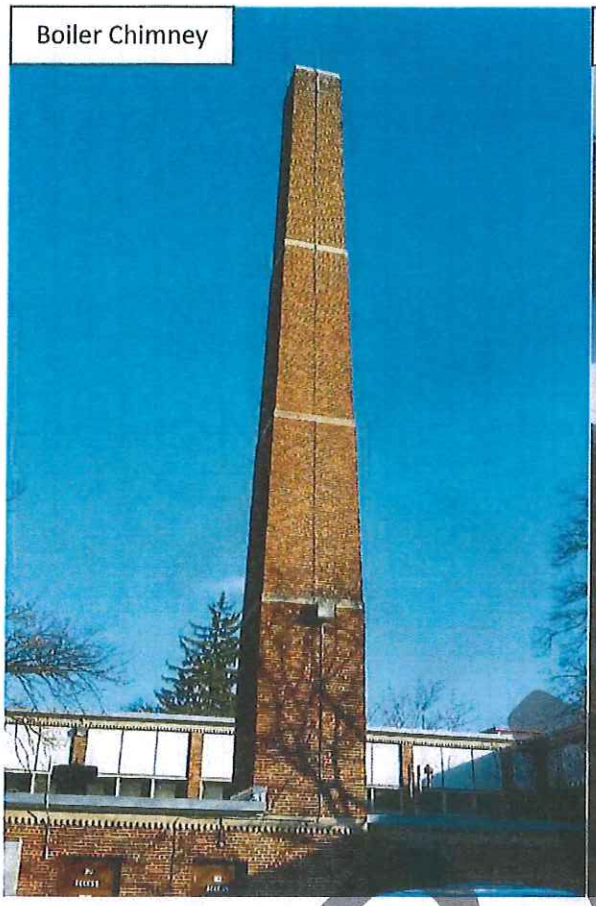

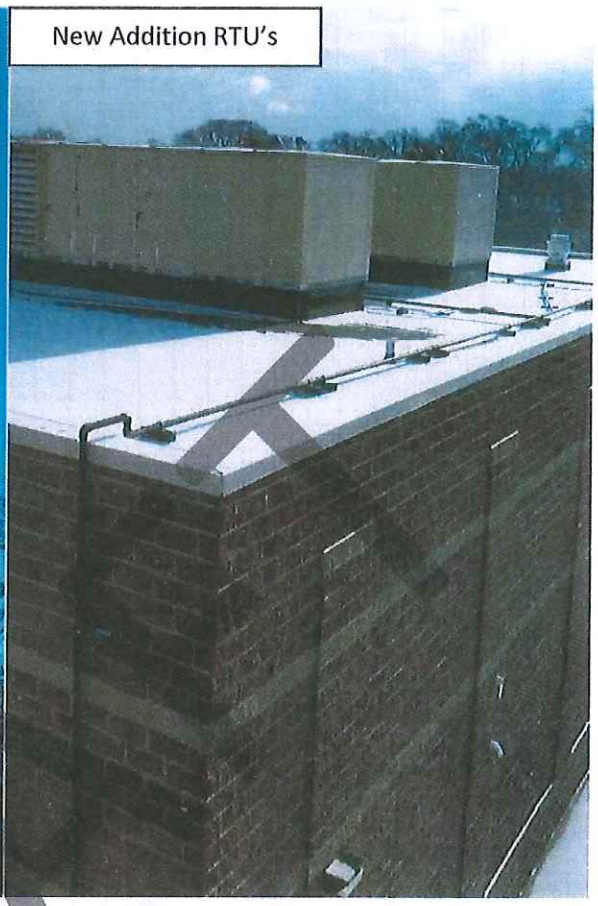

DRAFT

BUILDING

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St Detroit Mi	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days		BUILDING
1	POOR	Worn from use -end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	John Tisdale	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
Civil							
	Perimeter Fencing		3				
	Paving Parking Lot (Asphalt / Concrete)						condition was not visible due to snow
	Curbing		3				
	On-Site Signage		3				
	Pedestrian Access (Michigan Barrier Free & Safety)		3				
Site Facilities							
	Loading Dock		3				
Michigan barrier free Compliance							
	Handicap Parking					N/A	
	Accessible Entry		3				
	Exterior Ramps and walks		3				
	Barrier free route (ROW - Sidewalk to Bldg. Entry)		3				
	Building Entry		3				
Foundation/Footings							
	Structure		3				
Columns/Beams/Walls							
	Structure		3				
	Applied Fireproofing Systems					N/A	
Roofing							
	Roof Openings (Skylights)					N/A	
	Roof Openings (Access)					N/A	
	Roof Equipment Curbing		3				
	Leakage		3				
	Ponding Water		3				
	Roof Drains		3				
	Gutters / Downspouts		3				
Exterior Walls							
	Exterior Finish		3				

DRAFT

BUILDING

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St Detroit Mi	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days		BUILDING
1	POOR	Worn from use -end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	John Tisdale	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
	Expansion / Control Joints		3				
	Thermal Condition		3				
	Soffits		3				
	General Appearance		3				
Doors / Windows / Louvers							
	Windows		3				
	Louvers and Vents					N/A	
	Main Entry Doors		3				
	Main Entry Hardware		3				
	Other Exterior Doors		3				
	Other Exterior Door Hardware		3				
General							
	Wall Finishes (Classrooms)		3				
	Wall Finishes (Corridors)		3				
	Wall Finishes (Restrooms)		3				
	Wall Finishes (Others)		3				
	Ceilings		3				
	Cabinetry		3				
	Moveable / Operable Walls					N/A	
Interior Doors							
	Door & Frame Condition			2			
	Hardware Condition			2			
	Hallway Fire Door					N/A	
	Cafe / Concession Security Gates / Roll-up Doors					N/A	
Flooring							
	ACT					N/A	
	Drywall					N/A	
	Other					N/A	
	Carpet					N/A	

DRAFT

BUILDING

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St Detroit Mi	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days		BUILDING
1	POOR	Worn from use-end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	John Tisdale	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
	VCT					N/A	
	Tile		3				
	Terrazzo		3				
	Wood		3				
	Sealed Concrete						
Stairs							
	Landing finish		3				
	Stair treads		3				
	Stair nosings		3				
	Handrails		3				
Toilet Rooms							
	Flooring		3				
	Walls		3				
	Signage		2				

***Any violations reported in this school assessment were not given to the facility as violations to be corrected in order to maintain the certificate of occupancy for the

DRAFT

MECHANICAL

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St Detroit Mi	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days	Built 1923	BUILDING
1	POOR	Worn from use -end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	Jon Paradine	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
Gas System							
	Piping			2			
	Other (Vented Interior Regulators)			2			
	Gas PRV (Proximity to OA intakes)			2			
	Science Classroom Emergency Off Switch					NA	
Cooling Plant							
	Distribution Piping (2 pipe or 4-pipe)					NA	
	Chillers (Age, Refrigerant, Heat Rejection Method)					NA	
	Cooling Towers (Age, Materials, VFD, Sufficiency)					NA	
	CHW Pump Volute Insulation type (foamglass, Armaflex, phenolic foam, fiberglass, mineral wool)					NA	
	Plant Piping & Valves (Corroded/Isolation valves)					NA	
	Chilled Water Pipe Insulation & Jacket (Foamglass Armaflex					NA	
	Campus Piping & Valves (Corroded/Isolation valves)					NA	
	Refrigeration Room Monitoring and Ventilation					NA	
Heating Plant							
	Boilers (Age, Fuel Type, Input/Output)			2			
	Pumps (VFD / Sound / Suction Pressure)			2			
	Plant Piping & Valves (Corroded/Isolation valves)			2			
	Campus Piping & Valves (Corroded/Isolation valves)			2			
	Boiler Room E-Stop					NA	
Dedicated Airside Heating Systems							
	Heating-Only Air Handling Units (Age)		3				
	Duct Furnaces (Fuel, Type, Age, Mission)			2			
	Unit Heaters (Fuel, Type, Age, Mission)			2			
	Heating-Only Unit Ventilators (year, condition)			2			
Air Distribution							
	Outside Air Units (Age, HR Type, ERV, Unitary, VAV)			2			
	Rooftop ACUs (Age, Gas Heat or Heat Pump)			2			

DRAFT

MECHANICAL

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St Detroit Mi	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days	Built 1923	BUILDING
1	POOR	Worn from use -end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	Jon Paradine	SURVEYOR

			4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
	Central Station AHUs (Age, Type/Geometry, VAV, typ. SAT dual path unit)				2			
	Terminal Units (VAV, VAV/reheat, Heat source, Close- off VAV, SFPU, PFPU)				2			
Exhaust Systems								
	Restrooms				2			
	Locker Rooms						NA	
	Kitchen	Hood Systems (Grease or Heat only, Ansul system, Heat sensor start)		3				
		Exhaust Fan Outlet height (Is it <40")		3				
	Science	Room Emergency Exhaust (Operation)						
		Fume Exhaust (Latest year certified, sash height, manifolded, VAV, fan location)			2			
		Stack outlet height (is it <10')			2			
	Art Kiln	Exhaust Fan / Exhaust Hood					NA	
Refrigeration Systems								
	Freezer Systems (Age, Location, Refrigerant)			3				
	Cooler Systems (Age, Location, Refrigerant)			3				
Indoor Swimming Pool Systems								
	Vent and Pool Heater						NA	
Fire Alarm System and Fire Suppression								
	Fire suppression				2			

***Any violations reported in this school assessment were not given to the facility as violations to be corrected in order to maintain the certificate of occupancy for the facility. Any violations reported in this school assessment were not cited as part of a school safety inspection, they are strictly for the use of the assessment report.

DRAFT

PLUMBING

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St. Detroit MI	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days	1923	BUILDING
1	POOR	Worn from use-end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	Kole Myers	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
Site Utilities							
	Backflow Preventer			2			Boiler room/no test reports
	Water Service Piping			2			
2							
	Roof Drains (piping)			2			
Toilet Rooms							
	Toilet Partitions			2			
General							
	Custodial Closets (Mop Sinks)			2			
	Laboratory Sinks					NA	
	Eyewash / Emerg. Shower (Tepid Water)					NA	
	Showers (Self metering, Shutoff)					NA	
	Kitchen (POU Grease, Interceptor)		3				
	Grease (Indoor/outdoor, Interceptor)					NA	
	Water Fountains (Self contained water cooler, bubbler)			2			
	Sewer Ejector systems			2			
	Dilution Tanks (Science Classrooms/Neutralization tanks)					NA	
	DWV			2			
Restrooms							
	Water Closets			2			
	Urinals			2			
	Lavatories / Sinks			2			
Water Distribution							
	Water Distribution Piping			2			all covered
	Water Heaters (Separate from Bldg. Heating / Kitchen)		3				2010 kitchen remodel/ 2 for exhisting bldg
	Water Meter			2			
Food Service							
	SS Sinks		3				2010 upgrade
	Mop Sinks		3				2010 upgrade

DRAFT

PLUMBING

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St. Detroit MI	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days	1923	BUILDING
1	POOR	Worn from use-end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	Kole Myers	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
	Water and Drains		3				2010 upgrades
Domestic Water Heating							
	Dedicated Heater for Kitchen		3				
	Recirculation Pump (Operating- Yes/No)			2			

***Any violations reported in this school assessment were not given to the facility as violations to be corrected in order to maintain the certificate of occupancy for the facility. Any violations reported in this school assessment were not cited as part of a school safety inspection, they are strictly for the use of the assessment report.

DRAFT

BOILER

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St Detroit Mi	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days	Built 1923	BUILDING
1	POOR	Worn from use end of expected lifecycle	Violations-45 days	42775	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	Jon Paradine	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
Heating Plant							
	Boilers (Age, Fuel Type, Input/Output)			2			
	Pumps (VFD / Sound / Suction Pressure)			2			
	Plant Piping & Valves (Corroded/Isolation Valves)			2			

***Any violations reported in this school assessment were not given to the facility as violations to be corrected in order to maintain the certificate of occupancy for the facility. Any violations reported in this school assessment were not cited as part of a school safety inspection, they are strictly for the use of the assessment report.

DRAFT

ELEVATOR

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St Detroit Mi	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days	Built 1923	BUILDING
1	POOR	Worn from use-end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	Jon Paradine	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
Elevator State Serial Number:							
	Machine Room Equipment					N/A	
	Door Operators and Operating Equipment					N/A	
	Interior Cab / Signage / Emerg. Phone					N/A	
	Hoistway Pit					N/A	
	Landing Fixtures					N/A	
	Operating Condition					N/A	
	Ropes / Hoisting Equipment					N/A	
	Hoistway Equipment					N/A	
	Fire and Emergency Service					N/A	

***Any violations reported in this school assessment were not given to the facility as violations to be corrected in order to maintain the certificate of occupancy for the facility. Any violations reported in this school assessment were not cited as part of a school safety inspection, they are strictly for the use of the assessment report.

DRAFT

ELECTRICAL

4	NEW	New or like-new condition; no issues to report; no expected failures	No issues / violations or adverse conditions / less than 3 years old	Robert Burns Elementary	SCHOOL NAME
3	GOOD	Good condition; no reported issues or concerns	No issues / violations or adverse conditions other than new	14350 Terry St, Detroit, MI	ADDRESS
2	FAIR	Average wear for building age; not new but no issues	Violations-90 days	School	BUILDING
1	POOR	Worn from use -end of expected lifecycle	Violations-45 days	2/9/2017	SURVEY DATE
0	CRITICAL	Extremely worn or damaged	Violations / Imminent danger or inoperable	Lance Ash	SURVEYOR

		4	3	2	1	0	COMMENTS / RECOMMENDED ACTION
Electrical Supply							
	Service Switchgear/Electrical Service (Observed Condition)			2			
	District-owned Site Transformers (Observed Condition)			2			
	Motor Control Centers			2			
Electrical Distribution							
	Equipment			2			
	Panelboards (Condition & Capacity)			2			
	Feeders (Observed Condition)			2			
	Devices (Switches & Receptacles)			2			
	TSS - Surge Suppression					NA	
	Transformers		3				It appears that a new primary transformer
Lighting							
	Classroom (Instructional)			2			
	Corridor / Common Areas			2			
	Restrooms			2			
	High Bay Areas			2			Metal halide light fixtures inside the
	Emergency (Condition & Code Compliance)			2			Several exit lights throughout the building
	Exterior Perimeter (Building Mounted)			2			
	Lighting Controls (Building Level)			2			
Other							
	Kitchen Equipment Supply		3				
	Emergency Generator (Observed Condition)					NA	
	Intercom / PA Systems (Observed Condition)			2			
	Fire Alarm System (Observed Condition)			2			

***Any violations reported in this school assessment were not given to the facility as violations to be corrected in order to maintain the certificate of occupancy for the facility. Any violations reported in this school assessment were not cited as part of a school safety inspection, they are strictly for the use of the assessment report.

DRAFT

Appendix C: School Quality Maps

DRAFT

Burns ES - MS: Qualified Schools Within 5 Miles

February 18, 2017

Est. Service Area

Schools

Elementary School

ES-MS

Middle School

Most Grades (PK-12)

Selected School: Burns Elementary-Middle School

0 1.25 2.5 5 mi

0 2 4 8 km

Sources: Esri, HERE, DeLorme, USGS, Intermap, INCREMENT P, NRCan, Esri Japan, METI, Esri China (Hong Kong), Esri Korea, Esri (Thailand),

Area Schools radius: 5 Miles | Map: State of Michigan - CSS (2017©)

Burns ES - MS: Qualified Schools Within 10 Miles

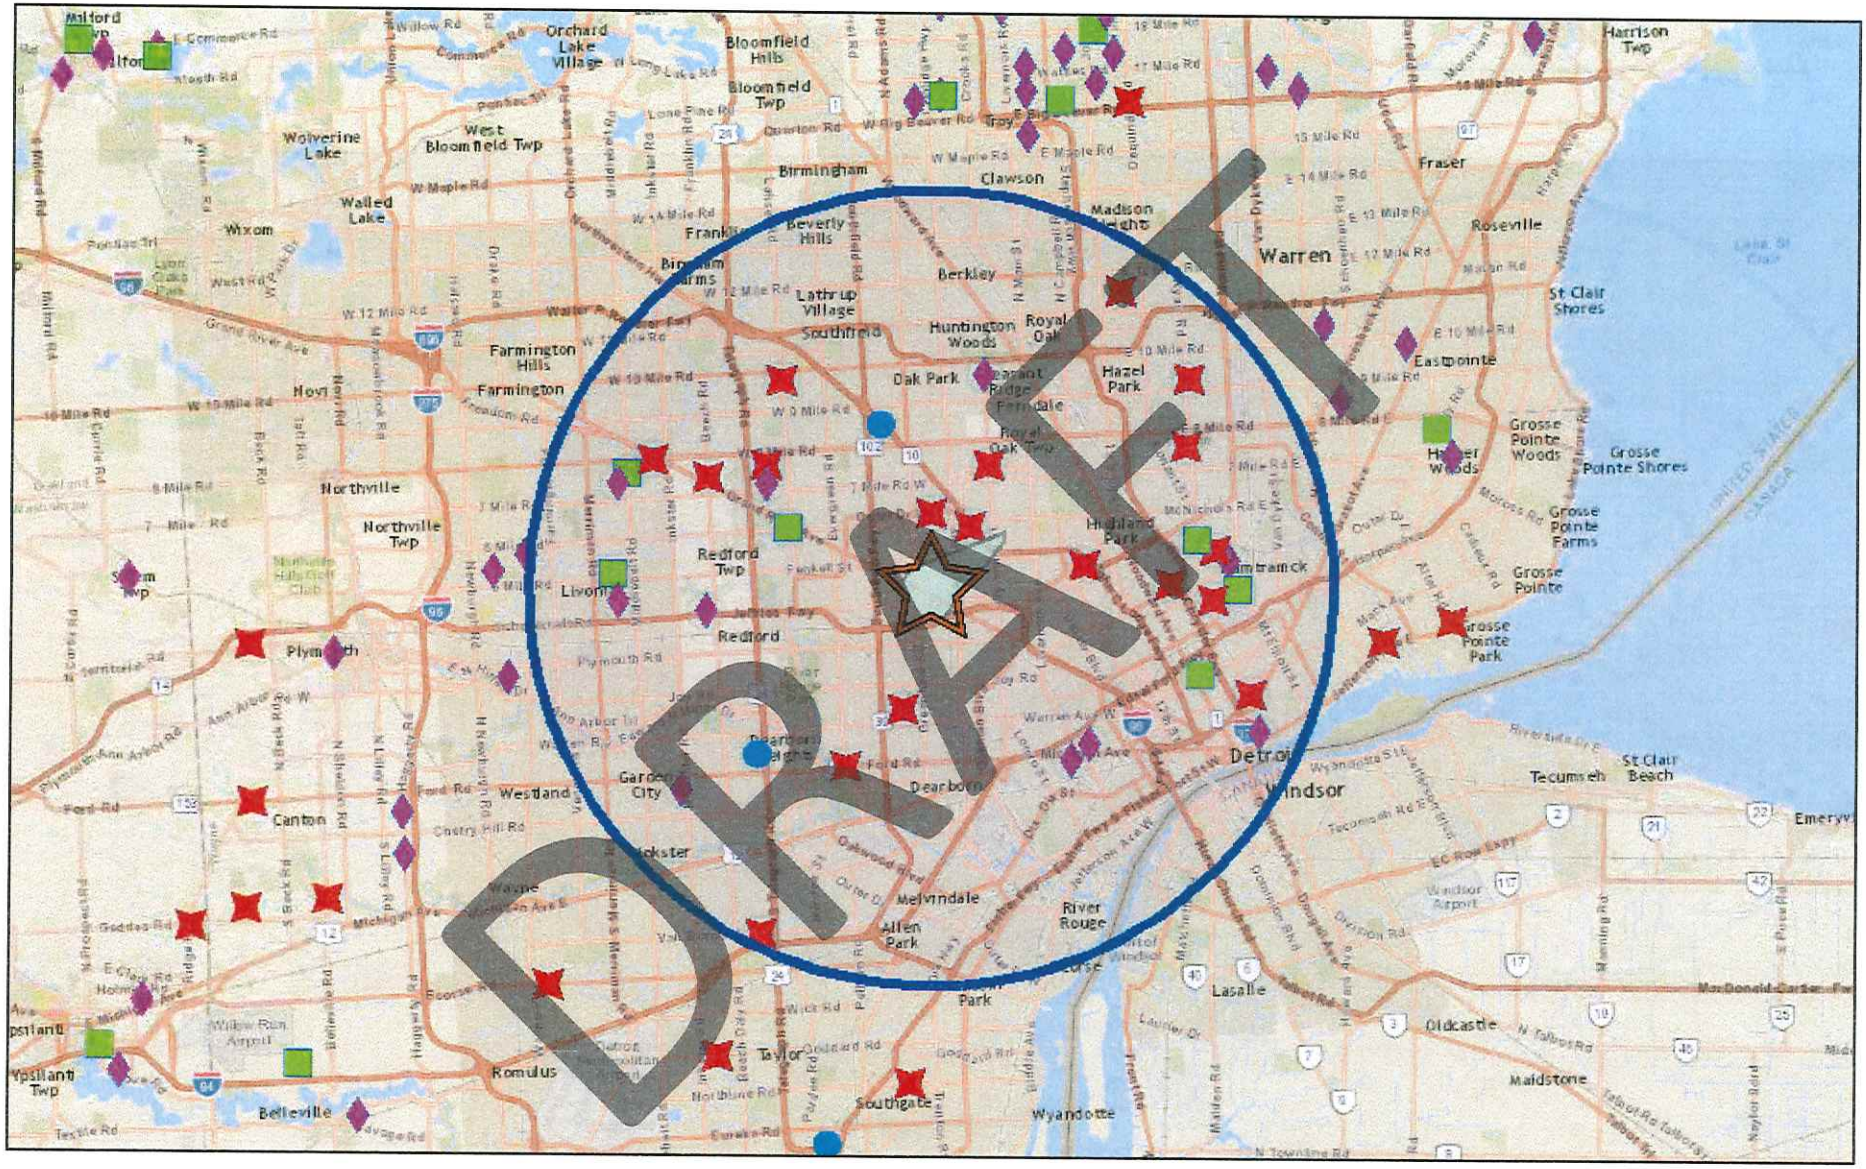

February 18, 2017

Est. Service Area

Schools

Elementary School

ES-MS

Middle School

Most Grades (PK-12)

Selected School: Burns Elementary-Middle School

0 2.5 5 10 mi

0 4 8 16 km

Sources: Esri, HERE, DeLorme, USGS, Intermap, INCREMENT P, NRCan, Esri Japan, METI, Esri China (Hong Kong), Esri Korea, Esri (Thailand),

Area Schools radius: 10 Miles | Map: State of Michigan - CSS (2017©)

Burns ES - MS: Qualified Schools Within15 Miles

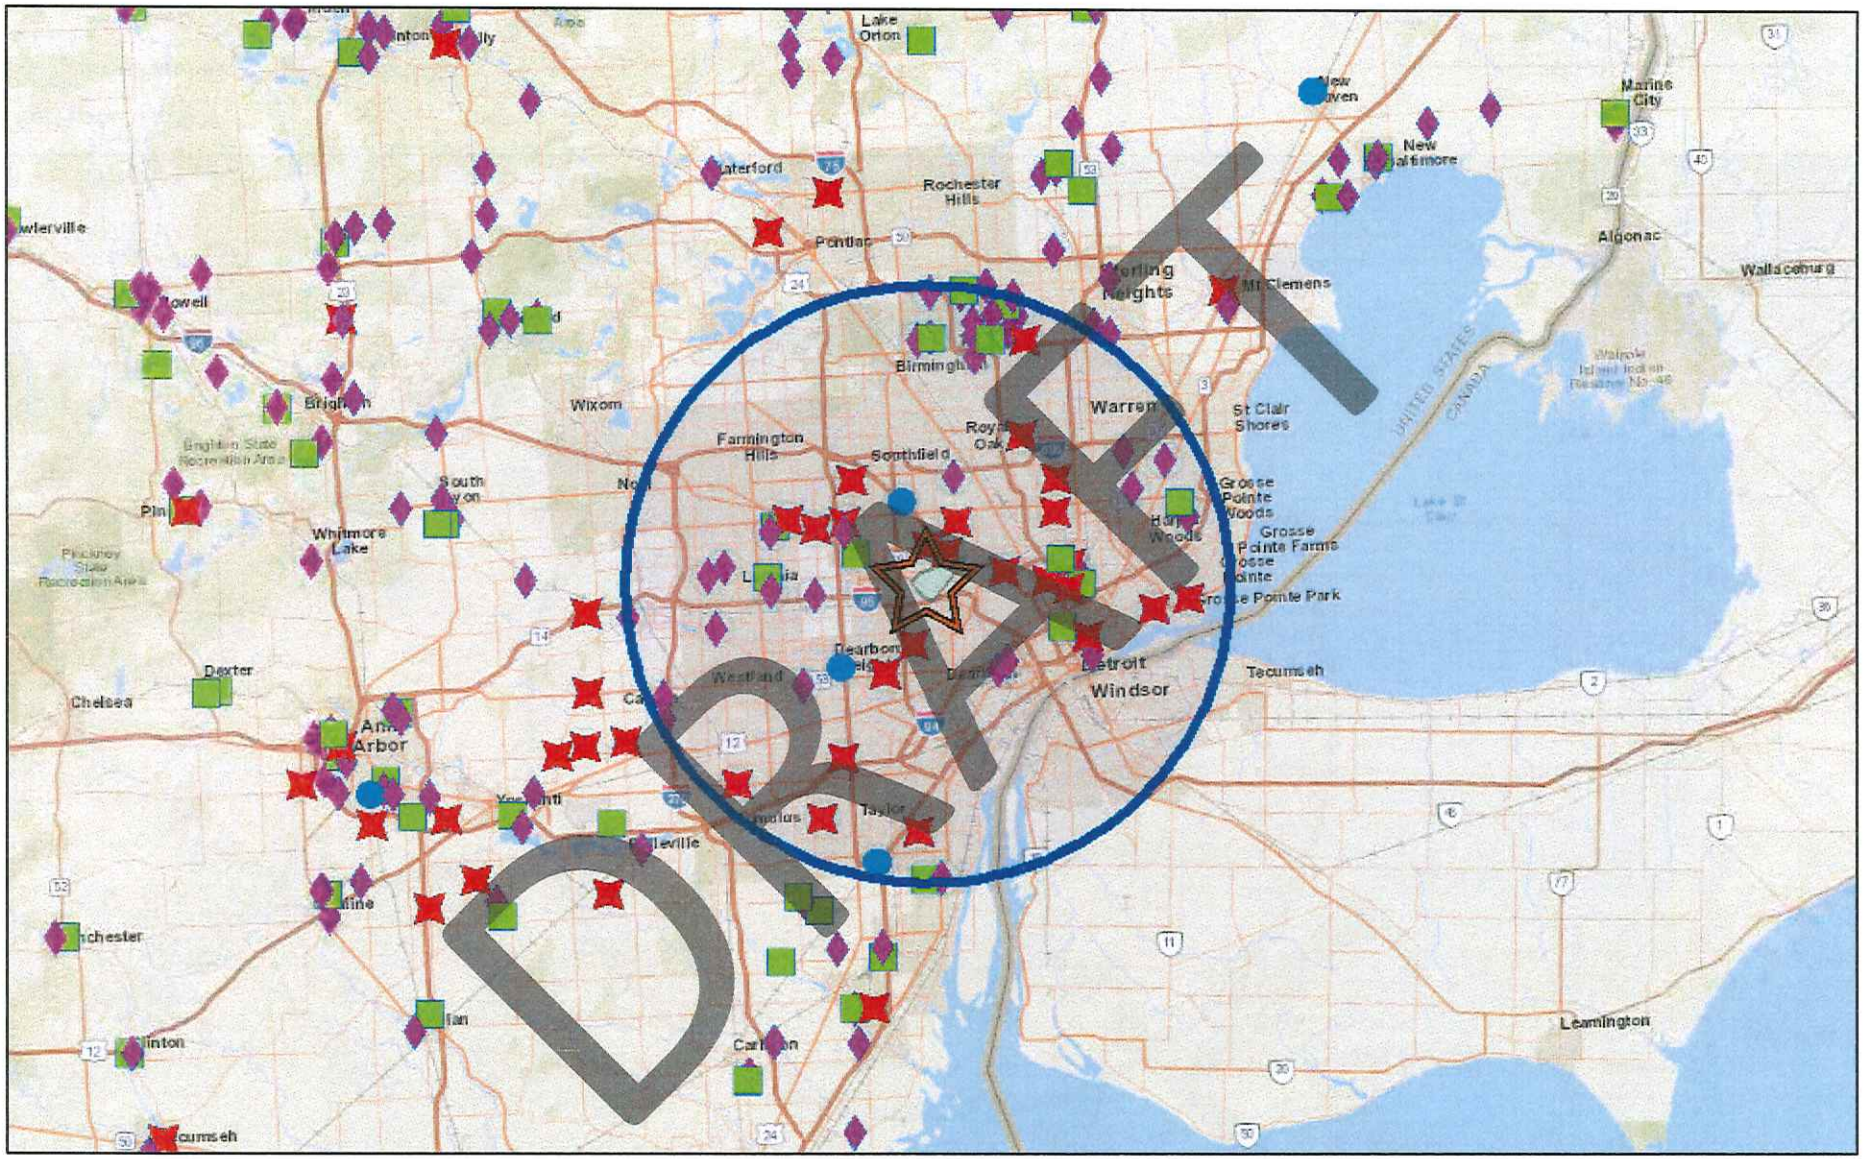

February 18, 2017

Est. Service Area

Schools

Elementary School

ES-MS

Middle School

Most Grades (PK-12)

Selected School: Burns Elementary-Middle School

0 5 10 20 mi

0 5 10 20 km

Sources: Esri, HERE, DeLorme, USGS, Intermap, INCREMENT P, NRCan, Esri Japan, METI, Esri China (Hong Kong), Esri Korea, Esri (Thailand),

Area Schools radius: 15 Miles | Map: State of Michigan - CSS (2017©)

Burns ES - MS: Qualified Schools Within 20 Miles

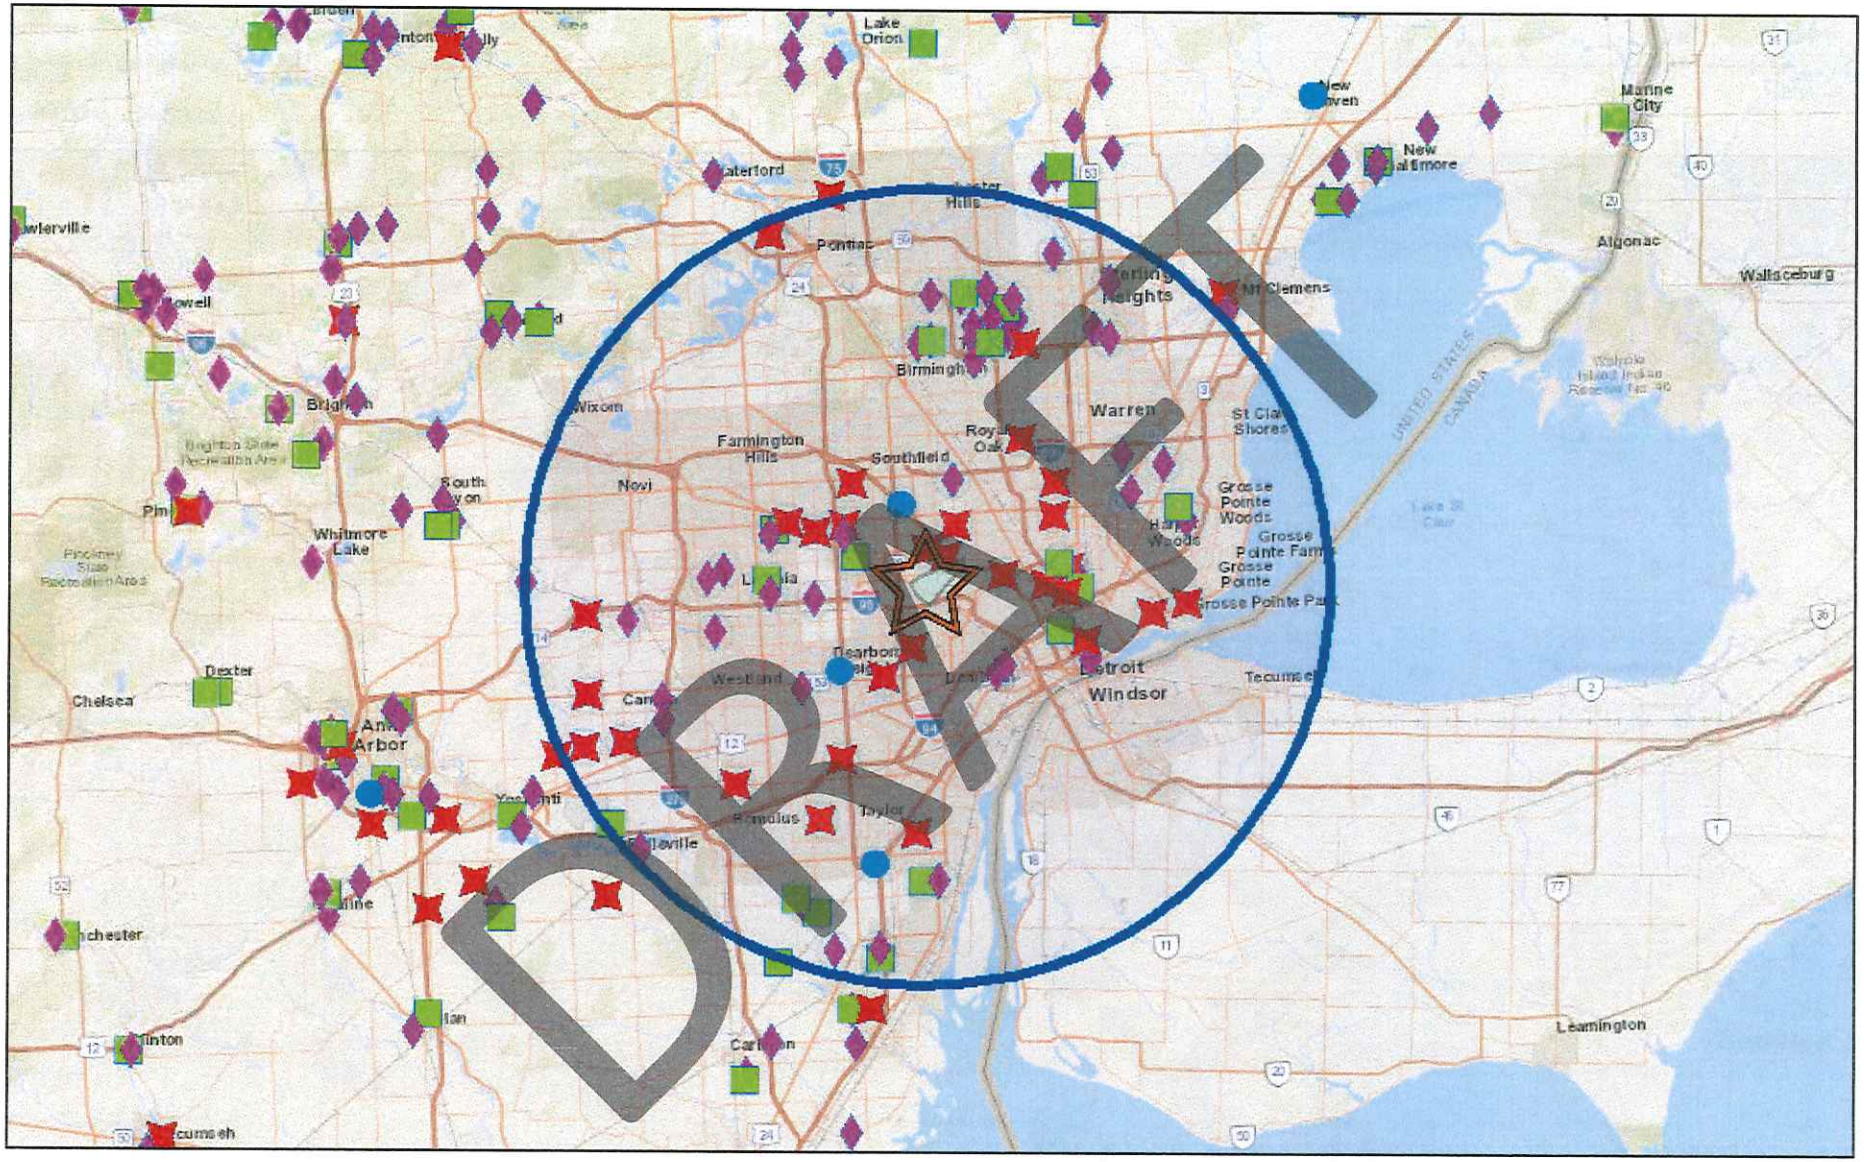

February 18, 2017

Est. Service Area

Schools

Elementary School

ES-MS

Middle School

Most Grades (PK-12)

Selected School: Burns Elementary-Middle School

0 5 10 20 mi

0 5 10 20 km

Sources: Esri, HERE, DeLorme, USGS, Intermap, INCREMENT P, NRCan, Esri Japan, METI, Esri China (Hong Kong), Esri Korea, Esri (Thailand),

Area Schools radius: 20 Miles | Map: State of Michigan - CSS (2017©)

Burns ES - MS: Qualified Schools Within 25 Miles

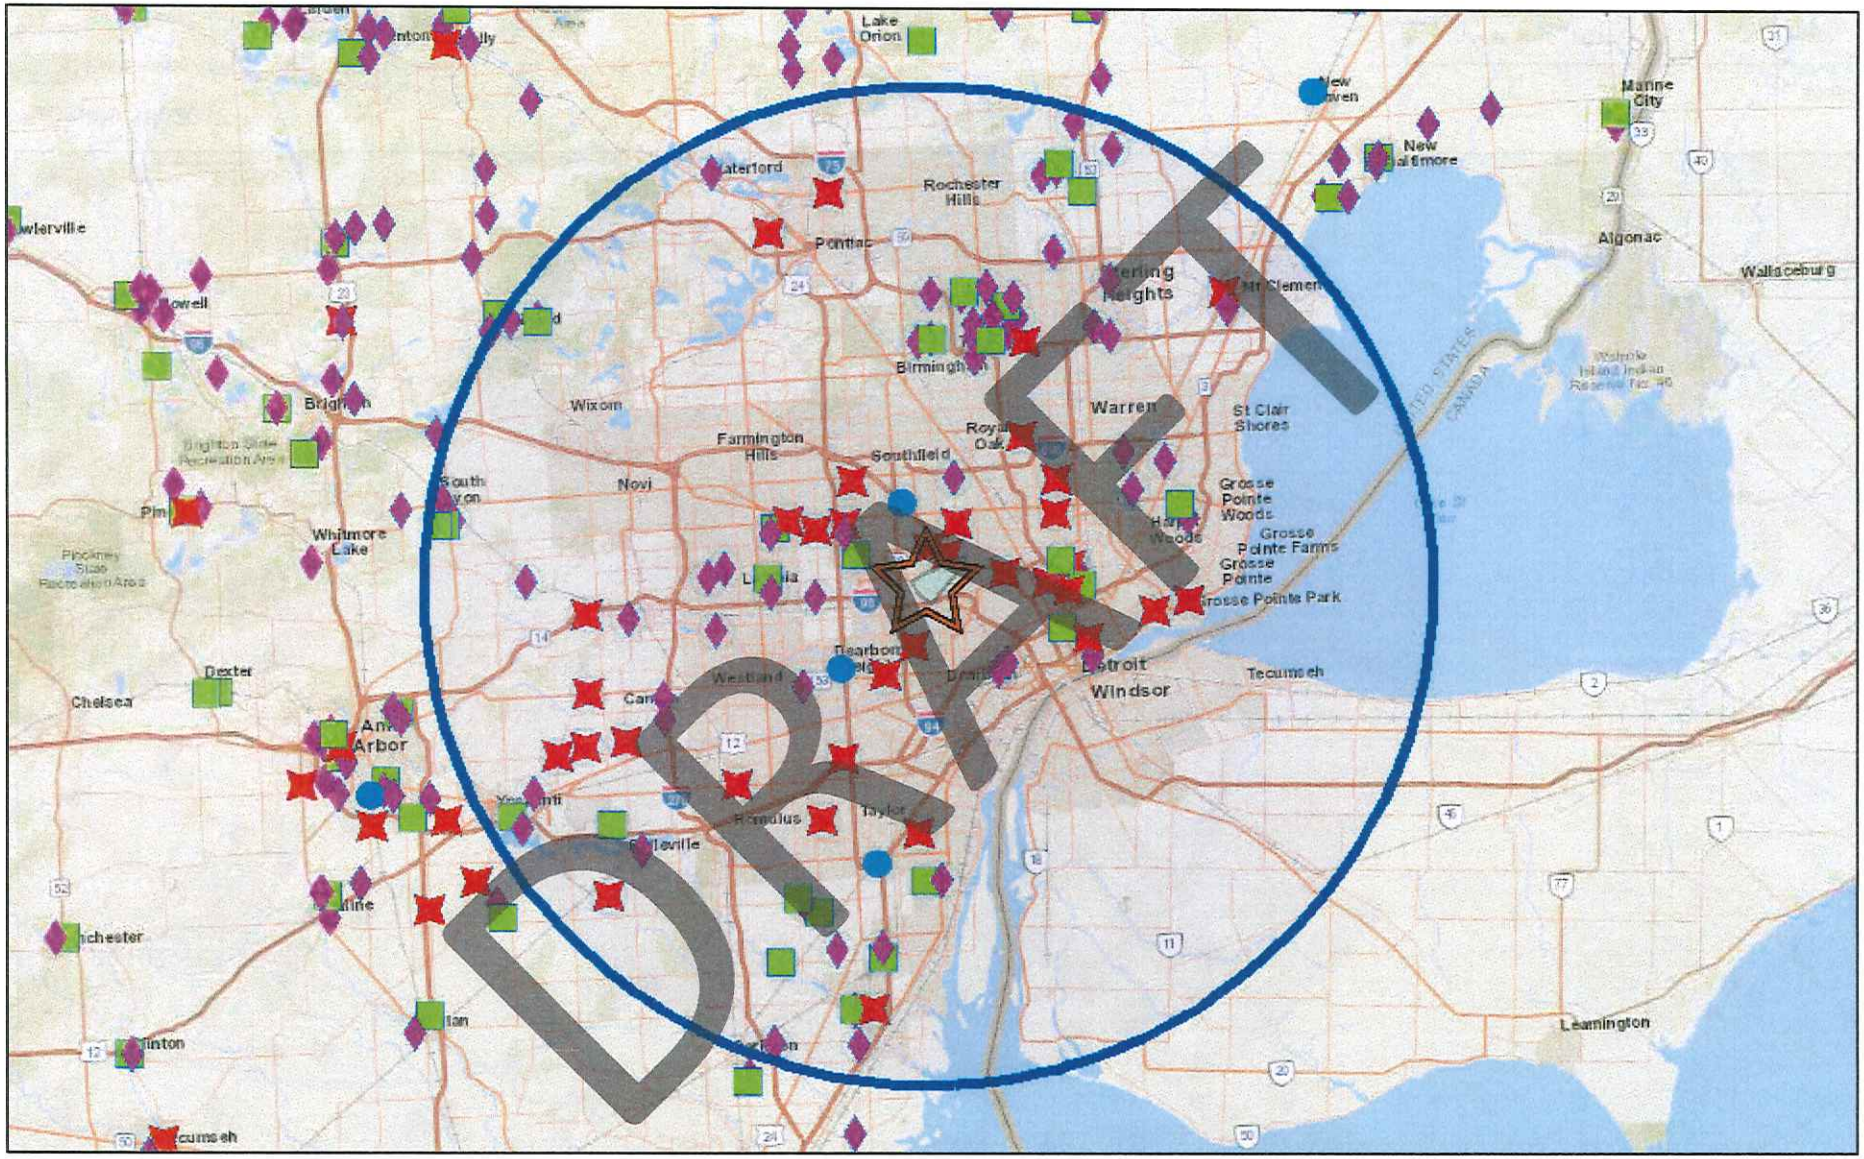

February 18, 2017

Est. Service Area

Schools

Elementary School

ES-MS

Middle School

Most Grades (PK-12)

Selected School: Burns Elementary-Middle School

0 5 10 20 mi

0 5 10 20 km

Sources: Esri, HERE, DeLorme, USGS, Intermap, INCREMENT P, NRCan, Esri Japan, METI, Esri China (Hong Kong), Esri Korea, Esri (Thailand).

Area Schools radius: 25 Miles | Map: State of Michigan - CSS (2017©)

Burns ES - MS: Qualified Schools Within 30 Miles

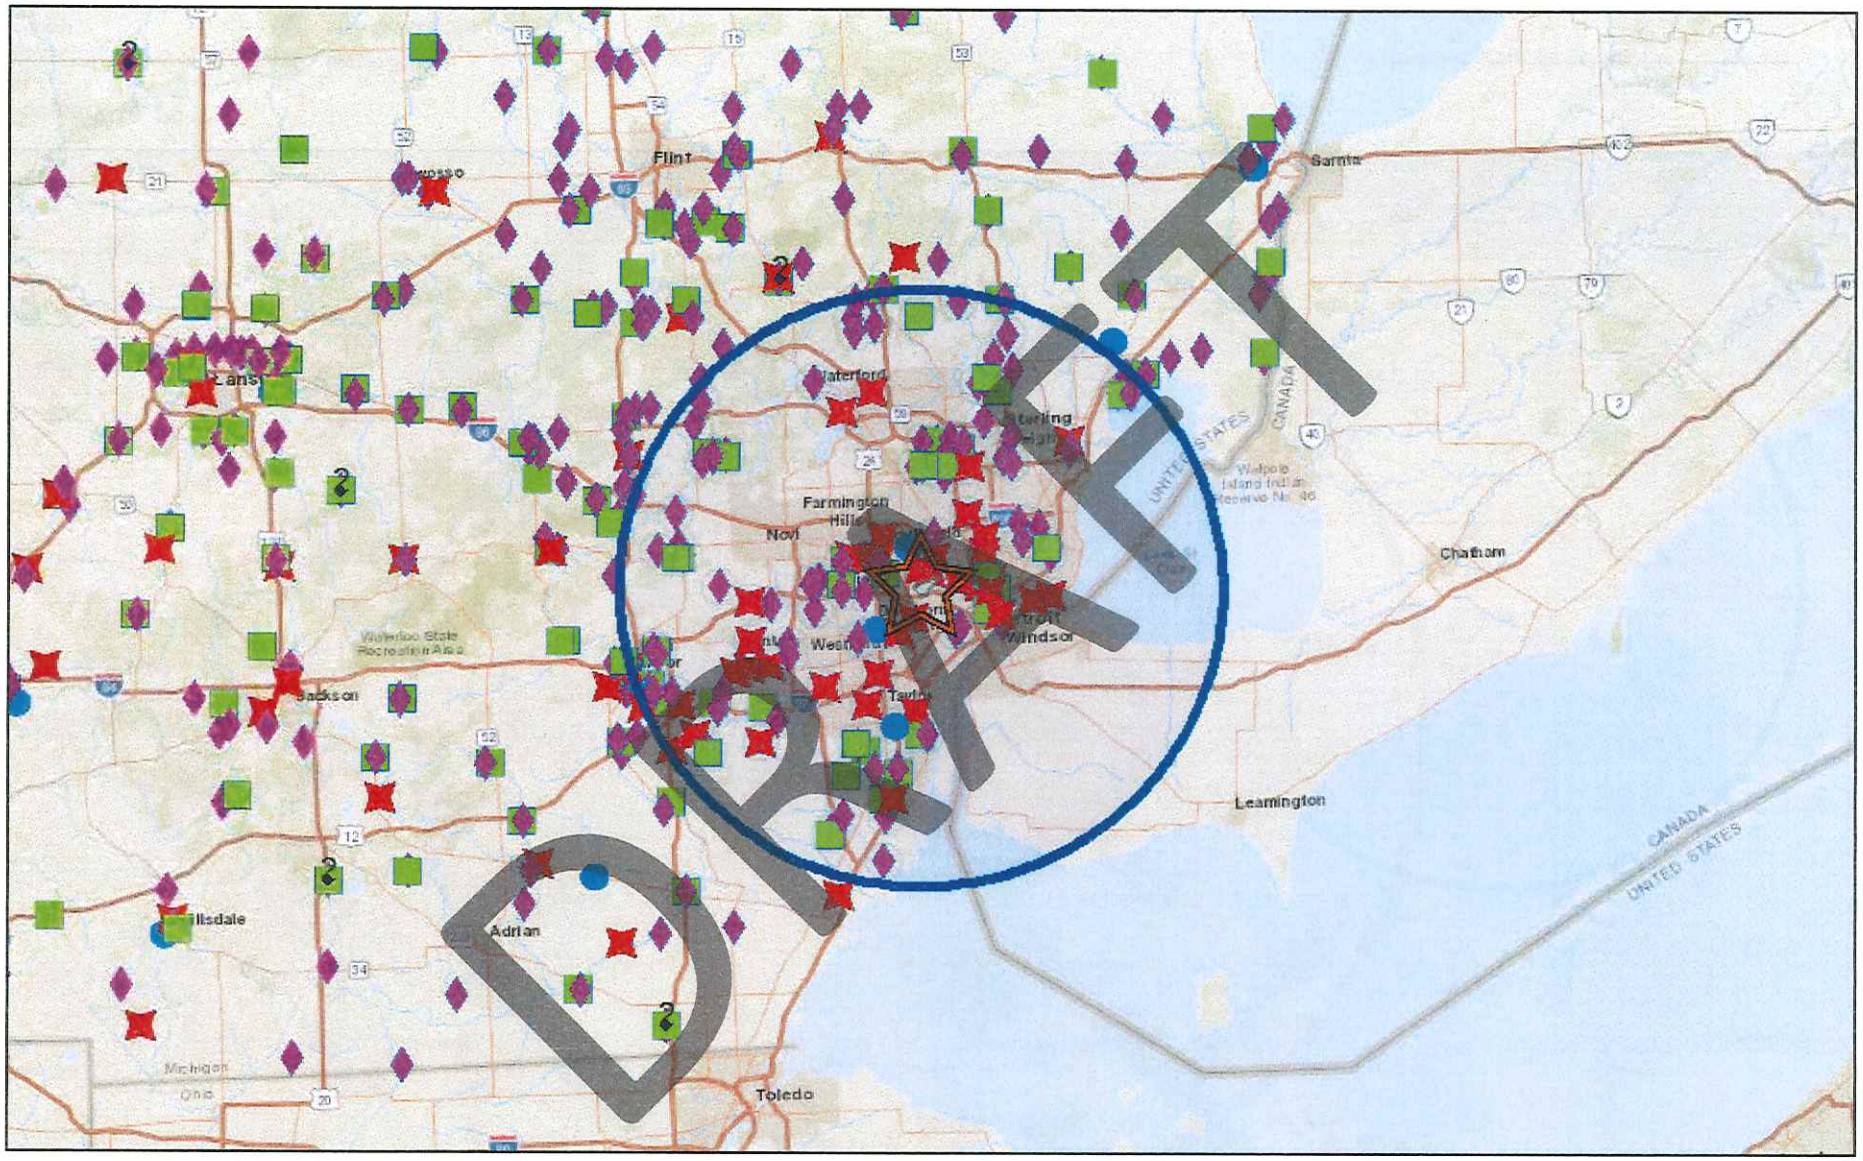

February 18, 2017

Est. Service Area

Schools

Elementary School

ES-MS

Middle School

Most Grades (PK-12)

Selected School: Burns Elementary-Middle School

0 10 20 40 mi

0 15 30 60 km

Sources: Esri, HERE, DeLorme, USGS, Intermap, INCREMENT P, NRCan, Esri Japan, METI, Esri China (Hong Kong), Esri Korea, Esri (Thailand),

Area Schools radius: 30 Miles | Map: State of Michigan - CSS (2017©)

Appendix D: Financial Impact

DRAFT

Appendix C: Financial Impact

Schools Identified for the Next Level of Accountability Outstanding Obligations	
Education Achievement Authority of Michigan	
Loan Balance	**Maturity**
DOES NOT PARTICIPATE IN MFA SAN	

Source: Michigan Department of Treasury via the Michigan Finance Authority

Appendix C: Financial Impact

Schools' Potential Losses from School Closures						
Schools	**Allowance**	**Student Count (Losing)**	**Foundation (Losing)**	**Student Count (Total)**	**Foundation (Total)**	**% of Foundation**
Burns Elementary-Middle School	$ 7,552.00	468.00	$ 3,534,336.00	5,079.94	$ 38,363,706.88	9.21%
Denby High School	$ 7,552.00	604.00	$ 4,561,408.00	5,079.94	$ 38,363,706.88	11.89%
Ford High School	$ 7,552.00	435.00	$ 3,285,120.00	5,079.94	$ 38,363,706.88	8.56%
Law Elementary School	$ 7,552.00	585.00	$ 4,417,920.00	5,079.94	$ 38,363,706.88	11.52%
Mary McLeod Bethune Elementary-Middle School	$ 7,552.00	532.00	$ 4,017,664.00	5,079.94	$ 38,363,706.88	10.47%
Mumford High School	$ 7,552.00	742.00	$ 5,603,584.00	5,079.94	$ 38,363,706.88	14.61%

Appendix C: Financial Impact *(continued)*

Education Achievement Authority of Michigan						
Schools' Potential Losses from School Closures						
Schools	**Allowance**	**Student Count (Losing)**	**Foundation (Losing)**	**Student Count (Total)**	**Foundation (Total)**	**% of Foundation**
Pershing High School	$ 7,552.00	329.00	$ 2,484,608.00	5,079.94	$ 38,363,706.88	6.48%
Southeastern High School	$ 7,552.00	284.00	$ 2,144,768.00	5,079.94	$ 38,363,706.88	5.59%
TOTAL	$ 7,552.00	3,979.00	$ 30,049,408.00	5,079.94	$ 38,363,706.88	78.33%
EAA 2016 Federal Revenues	**General Fund**	$ 22,381,136.39				
	Total	$ 22,381,136.39				

Source: Michigan Department of Treasury
