Jackson & Mechanic Street Railroad Bridge Reconstruction

AECOM

Job Number: 204744 **Control Sections:** AML MP 75.79 & AML MP 75.94

Managing Office: Jackson TSC **Prime Contractor:** AnLaan

TSC Manager: Kelby Wallace, P.E. **Report Date:** Dec 28, 2022

Construction Engineer: Jason Fossit, P.E.

Mechanic Street Progress Photos

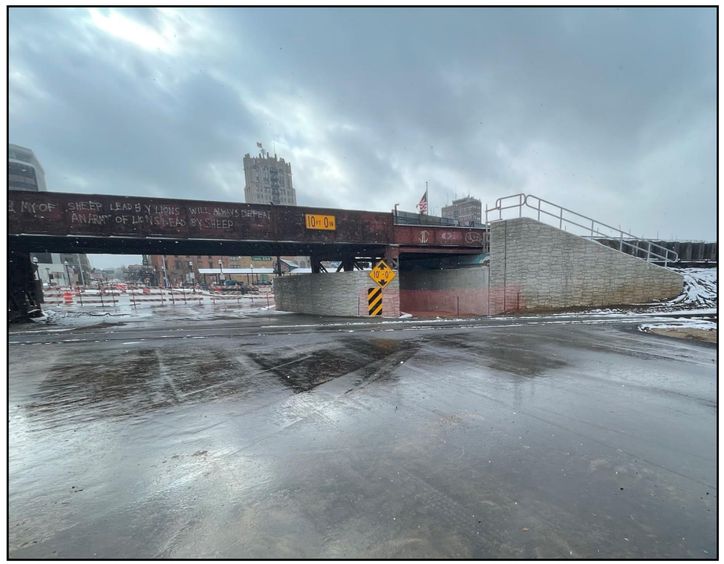

Railroad Grade Crossing Reconstructed and Paved w/ HMA - West Abutment 1 & 2

Mechanic Street paved w/ HMA & Temporary Sidewalk Open for Winter - Existing East Abutment & NE Retaining Wall

Project Costs

Awarded Contract Amount	$ 32,854,455.60
Authorized Contract Changes	$ 917,838.76
Pending Contract Changes	$ (280,515.15)
Current Contract Cost (Auth + Pend)	$ 33,491,779.21
Paid to Date	$ 16,629,676.59
Contract Balance Remaining	$ 16,862,102.62
% Complete (Current Cost)	49.65%
% Extras & Overruns (Awarded Cost)	1.94%

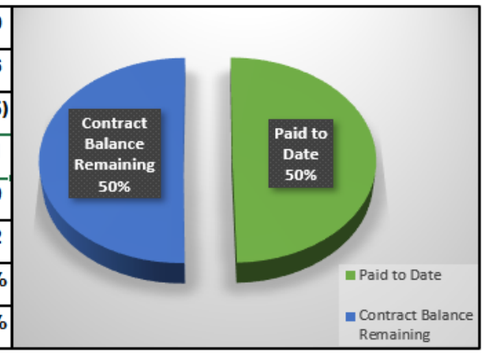

Jackson Street Progress Photos

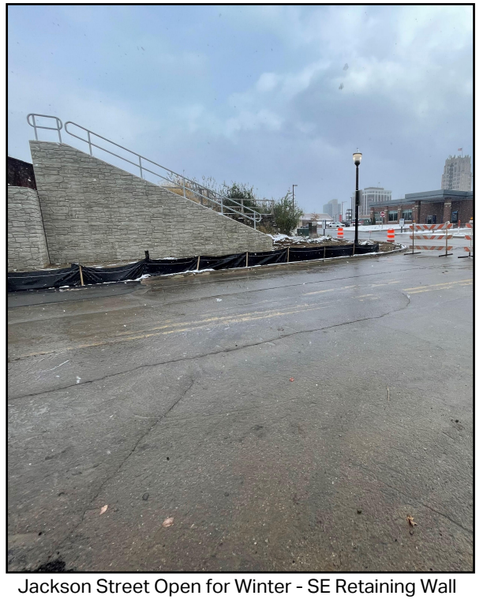

Jackson Street Open for Winter - SE Retaining Wall

Van Buren Street to Remain Closed Through Winter - West Abutment & SW Retaining Wall

Jackson Street HMA Patched - East Abutment

Drone Shots & Timelapse

Video Link (Click Here)
